Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
FF Aquarium Reno & Addition - BL 10.31.25		724	686	12-Sep-25 A	26-Jun-28
MILESTONES		631	631	05-Jan-26	26-Jun-28
MIL1010	Shark Tank Construction Start	0	0	05-Jan-26	
MIL1060	Renovation Construction Start	0	0	05-Jan-26	
MIL1020	Shark Tank Complete	0	0		26-Jun-28
MIL1040	Renovation Complete	0	0		26-Jun-28
MIL1070	Aquarium Ready to Open	0	0		26-Jun-28
PRECONSTRUCTION		86	55	12-Sep-25 A	02-Jan-26
PRE1160	Phase 1 GMP Submission/Review	45	15	15-Sep-25 A	31-Oct-25
PRE1170	Phase 1 Prep/Submit 100% CD Bid Set	10	10	13-Oct-25	24-Oct-25
Phase 1 Building Permit		40	55	09-Oct-25 A	02-Jan-26
BP1020	NCDEQ Review/Approve	40	55	09-Oct-25 A	02-Jan-26
BP1030	CAMA Review/Approve	40	55	09-Oct-25 A	02-Jan-26
Phase 1 Bidding		69	48	12-Sep-25 A	19-Dec-25
Release 1		69	48	12-Sep-25 A	19-Dec-25
R1 1070	Bidding Period	20	28	12-Sep-25 A	19-Nov-25
R1 1030	Bid Day	1	1	20-Nov-25	20-Nov-25
R1 1040	Re-Bid (If Needed)	8	8	21-Nov-25	04-Dec-25
R1 1050	Submit Bids to SCO/Reconcile	10	10	05-Dec-25	18-Dec-25
R1 1060	NTP Issued	1	1	19-Dec-25	19-Dec-25
PROCUREMENT		305	305	22-Dec-25	09-Mar-27
Bid & Award		10	10	22-Dec-25	07-Jan-26
A4440	Electrical - Award	10	10	22-Dec-25	07-Jan-26
A4450	Mechanical - Award	10	10	22-Dec-25	07-Jan-26
A4460	Plumbing - Award	10	10	22-Dec-25	07-Jan-26
A4470	Sprinkler - Award	10	10	22-Dec-25	07-Jan-26
A4480	Demo - Award	10	10	22-Dec-25	07-Jan-26
A4490	Sitework - Award	10	10	22-Dec-25	07-Jan-26
A4500	Structural Steel - Award	10	10	22-Dec-25	07-Jan-26
A4510	Drywall - Award	10	10	22-Dec-25	07-Jan-26
A4520	Concrete - Award	10	10	22-Dec-25	07-Jan-26
A4530	Flooring - Award	10	10	22-Dec-25	07-Jan-26
A4540	Paint - Award	10	10	22-Dec-25	07-Jan-26
A4550	Masonry - Award	10	10	22-Dec-25	07-Jan-26
A4560	Windows - Award	10	10	22-Dec-25	07-Jan-26
A4570	Roofing - Award	10	10	22-Dec-25	07-Jan-26
A5130	Doors - Award	10	10	22-Dec-25	07-Jan-26
A5140	LSS - Award	10	10	22-Dec-25	07-Jan-26
A5250	Acrylic Viewing Windows - Award	10	10	22-Dec-25	07-Jan-26
Steel		45	45	08-Jan-26	12-Mar-26
A4590	Prepare & Submit - Structural Steel	10	10	08-Jan-26	22-Jan-26
A4600	Review & Approve - Structural Steel	15	15	23-Jan-26	12-Feb-26
A4610	Fabricate & Deliver - Structural Steel	20	20	13-Feb-26	12-Mar-26
Concrete		65	65	08-Jan-26	10-Apr-26
STP1020	FRP Ship and Mangroves	65	65	08-Jan-26	10-Apr-26
A4980	Prepare & Submit - Concrete	10	10	08-Jan-26	22-Jan-26
A4990	Review & Approve - Concrete	15	15	23-Jan-26	12-Feb-26
A5000	Fabricate & Deliver - Concrete	20	20	13-Feb-26	12-Mar-26
LSS		220	220	08-Jan-26	17-Nov-26

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

FF Aquarium Reno & Addition - BL 10.31.25

11-Oct-25

Remaining Work Schedule

CLANCY & THEYS CONSTRUCTION COMPANY

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
A5100	Prepare & Submit - LSS	15	15	08-Jan-26	29-Jan-26
A5110	Review & Approve - LSS	15	15	30-Jan-26	19-Feb-26
A5120	Fabricate & Deliver - LSS Piping	30	30	20-Feb-26	02-Apr-26
A5210	Fabricate & Deliver - LSS Pumps & Filters	190	190	20-Feb-26	17-Nov-26
Electrical		295	295	08-Jan-26	09-Mar-27
Generator		295	295	08-Jan-26	09-Mar-27
A4620	Prepare & Submit - Generator	10	10	08-Jan-26	22-Jan-26
A4630	Review & Approve - Generator	15	15	23-Jan-26	12-Feb-26
A4640	Fabricate & Deliver - Generator	270	270	13-Feb-26	09-Mar-27
Lighting		55	55	08-Jan-26	26-Mar-26
A4890	Prepare & Submit - Lighting	10	10	08-Jan-26	22-Jan-26
A4900	Review & Approve - Lighting	15	15	23-Jan-26	12-Feb-26
A4910	Fabricate & Deliver - Lighting	30	30	13-Feb-26	26-Mar-26
Switchgear		285	285	08-Jan-26	23-Feb-27
A5150	Prepare & Submit - Switchgear	10	10	08-Jan-26	22-Jan-26
A5160	Review & Approve - Switchgear	15	15	23-Jan-26	12-Feb-26
EP4100	Fabricate & Deliver - Switchgear	260	260	13-Feb-26	23-Feb-27
ATS		205	205	08-Jan-26	27-Oct-26
A4920	Prepare & Submit - ATS	10	10	08-Jan-26	22-Jan-26
A4930	Review & Approve - ATS	15	15	23-Jan-26	12-Feb-26
A4940	Fabricate & Deliver - ATS	180	180	13-Feb-26	27-Oct-26
Misc. Electrical		45	45	08-Jan-26	12-Mar-26
A4950	Prepare & Submit - Misc. Electrical	10	10	08-Jan-26	22-Jan-26
A4960	Review & Approve - Misc. Electrical	15	15	23-Jan-26	12-Feb-26
A4970	Fabricate & Deliver - Misc. Electrical	20	20	13-Feb-26	12-Mar-26
Mechanical		65	65	08-Jan-26	10-Apr-26
RTUs		65	65	08-Jan-26	10-Apr-26
A4650	Prepare & Submit - RTUs	10	10	08-Jan-26	22-Jan-26
A4660	Review & Approve - RTUs	15	15	23-Jan-26	12-Feb-26
A4670	Fabricate & Deliver - RTUs	40	40	13-Feb-26	10-Apr-26
Exhaust Fans		65	65	08-Jan-26	10-Apr-26
A4860	Prepare & Submit - Exhaust Fans	10	10	08-Jan-26	22-Jan-26
A4870	Review & Approve - Exhaust Fans	15	15	23-Jan-26	12-Feb-26
A4880	Fabricate & Deliver - Exhaust Fans	40	40	13-Feb-26	10-Apr-26
Plubming		92	92	08-Jan-26	19-May-26
Domestic Water		45	45	08-Jan-26	12-Mar-26
A4800	Prepare & Submit - Domestic Water	10	10	08-Jan-26	22-Jan-26
A4810	Review & Approve - Domestic Water	15	15	23-Jan-26	12-Feb-26
A4820	Fabricate & Deliver - Domestic Water	20	20	13-Feb-26	12-Mar-26
Misc. Plumbing		45	45	08-Jan-26	12-Mar-26
A4680	Prepare & Submit - Misc. Plumbing	10	10	08-Jan-26	22-Jan-26
A4690	Review & Approve - Misc. Plumbing	15	15	23-Jan-26	12-Feb-26
A4700	Fabricate & Deliver - Misc. Plumbing	20	20	13-Feb-26	12-Mar-26
Sanitary / Storm		92	92	08-Jan-26	19-May-26
A5170	Prepare & Submit - Sanitary / Storm	10	10	08-Jan-26	22-Jan-26
A5180	Review & Approve - Sanitary / Storm	15	15	23-Jan-26	12-Feb-26
A5190	Fabricate & Deliver - Sanitary / Storm	67	67	13-Feb-26	19-May-26
Sprinkler		55	55	08-Jan-26	26-Mar-26
A4830	Prepare & Submit - Sprinkler	10	10	08-Jan-26	22-Jan-26
A4840	Review & Approve - Sprinkler	15	15	23-Jan-26	12-Feb-26

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

FF Aquarium Reno & Addition - BL 10.31.25

11-Oct-25

Remaining Work Schedule

CLANCY & THEYS CONSTRUCTION COMPANY

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
A4850	Fabricate & Deliver - Sprinkler	30	30	13-Feb-26	26-Mar-26
Roofing		45	45	08-Jan-26	12-Mar-26
A4710	Prepare & Submit - Roofing	10	10	08-Jan-26	22-Jan-26
A4720	Review & Approve - Roofing	15	15	23-Jan-26	12-Feb-26
A4730	Fabricate & Deliver - Roofing	20	20	13-Feb-26	12-Mar-26
Windows		65	65	08-Jan-26	10-Apr-26
A4740	Prepare & Submit - Windows	10	10	08-Jan-26	22-Jan-26
A4750	Review & Approve - Windows	15	15	23-Jan-26	12-Feb-26
A4760	Fabricate & Deliver - Windows	40	40	13-Feb-26	10-Apr-26
Acrylic Viewing Window		240	240	08-Jan-26	17-Dec-26
A5220	Prepare & Submit - Acrylic Viewing Windows	10	10	08-Jan-26	22-Jan-26
A5230	Review & Approve - Acrylic Viewing Windows	15	15	23-Jan-26	12-Feb-26
A5240	Fabricate & Deliver - Acrylic Viewing Windows	215	215	13-Feb-26	17-Dec-26
Doors & Frams		70	70	08-Jan-26	17-Apr-26
A4770	Prepare & Submit - Doors & Frames	10	10	08-Jan-26	22-Jan-26
A4780	Review & Approve - Doors & Frames	15	15	23-Jan-26	12-Feb-26
A4790	Fabricate & Deliver - Doors	45	45	13-Feb-26	17-Apr-26
A5200	Fabricate & Deliver - Door Frames	20	20	13-Feb-26	12-Mar-26
Finishes		65	65	08-Jan-26	10-Apr-26
Flooring		65	65	08-Jan-26	10-Apr-26
A4940	Prepare & Submit - Flooring	10	10	08-Jan-26	22-Jan-26
A5020	Review & Approve - Flooring	15	15	23-Jan-26	12-Feb-26
A5030	Fabricate & Deliver - Flooring	40	40	13-Feb-26	10-Apr-26
Drywall		45	45	08-Jan-26	12-Mar-26
A5040	Prepare & Submit - Drywall	10	10	08-Jan-26	22-Jan-26
A5050	Review & Approve - Drywall	15	15	23-Jan-26	12-Feb-26
A5060	Fabricate & Deliver - Drywall	20	20	13-Feb-26	12-Mar-26
Paint		45	45	08-Jan-26	12-Mar-26
A5070	Prepare & Submit - Paint	10	10	08-Jan-26	22-Jan-26
A5080	Review & Approve - Paint	15	15	23-Jan-26	12-Feb-26
A5090	Fabricate & Deliver - Paint	20	20	13-Feb-26	12-Mar-26
CONSTRUCTION		555	555	05-Jan-26	10-Mar-28
SOUTHEAST ADDITION		295	295	11-Sep-26	09-Nov-27
Sitework		65	65	11-Sep-26	14-Dec-26
A4210	Subgrade Cut & Fill	20	20	11-Sep-26	08-Oct-26
A4230	Install UG Chiller Piping	15	15	09-Oct-26	29-Oct-26
A4220	Footing Install	15	15	30-Oct-26	19-Nov-26
A4240	FRP Slab	15	15	20-Nov-26	14-Dec-26
Structure		25	25	15-Dec-26	21-Jan-27
A4250	Install CMU Walls	15	15	15-Dec-26	06-Jan-27
A4260	Install Roofing	10	10	07-Jan-27	21-Jan-27
Interior		105	105	15-Jun-27	09-Nov-27
R1-1080	Layout & Framing - Lv1 ST	10	10	15-Jun-27	28-Jun-27
A4270	Set Mechanical Pumps & Electrical Equipment	30	30	29-Jun-27	09-Aug-27
R1-1100	Install Plumbing In-Wall Rough - Lv1 ST	10	10	29-Jun-27	12-Jul-27
R1-1090	Install Electrical In-Wall Rough - Lv1 ST	15	15	29-Jun-27	19-Jul-27
F1-2350	Hang Drywall Walls - Lv1 ST	15	15	13-Jul-27	02-Aug-27
F1-2360	Tape & Finish Walls - Lv1 ST	20	20	03-Aug-27	30-Aug-27
F1-2370	Prime Paint - Lv1 ST	10	10	31-Aug-27	14-Sep-27

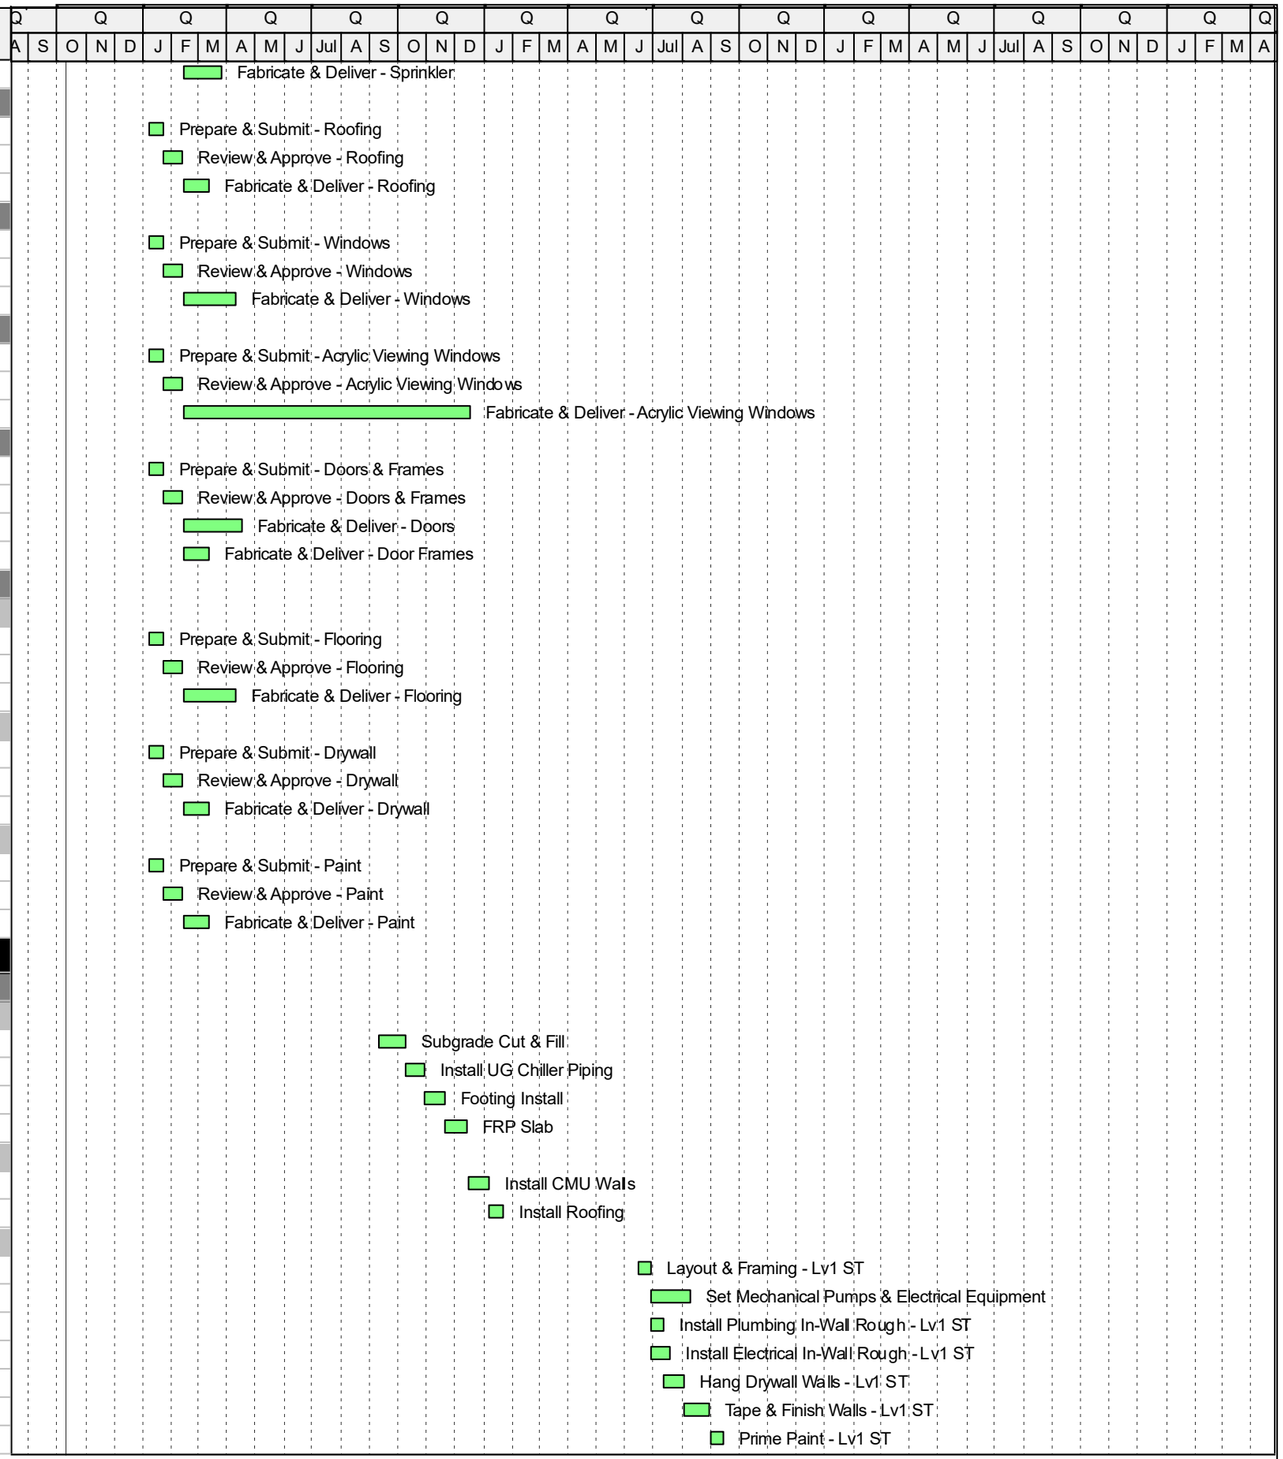

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

FF Aquarium Reno & Addition - BL 10.31.25

11-Oct-25
Remaining Work Schedule

CLANCY & THEYS CONSTRUCTION COMPANY

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
F1-2380	Install Lighting - Lv1 ST	20	20	15-Sep-27	12-Oct-27
F1-2390	Install Flooring - Lv1 ST	20	20	13-Oct-27	09-Nov-27
SHARK TANK		555	555	05-Jan-26	10-Mar-28
SITEWORK - ST		115	115	05-Jan-26	17-Jun-26
STS1010	Clearing and Grubbing	20	20	05-Jan-26	02-Feb-26
STS1000	Erosion Control	15	15	03-Feb-26	23-Feb-26
STS1020	Rough Grading/ Construction Entrance	20	20	24-Feb-26	23-Mar-26
STS1070	UG Domestic Water Install	15	15	03-Mar-26	23-Mar-26
STS1080	UG Domestic Water Shutdown/Swap Over	10	10	24-Mar-26	07-Apr-26
STS1090	Existing Storm Drain Removal	5	5	24-Mar-26	30-Mar-26
STS1100	Drainage Pond #2 Grade	15	15	31-Mar-26	21-Apr-26
STS1110	Employee Lot Storm Drain Install	15	15	22-Apr-26	12-May-26
Pump Station		60	60	24-Mar-26	17-Jun-26
STS1030	Pump Station Pad Prep	12	12	24-Mar-26	09-Apr-26
STS1040	Pump Station Building	15	15	10-Apr-26	30-Apr-26
STS1050	Pump Station Install	10	10	20-May-26	03-Jun-26
STS1060	Pump Station Shutdown/Swap Over	10	10	04-Jun-26	17-Jun-26
SUPERSTRUCTURE - ST		265	265	16-Jul-26	02-Aug-27
Shark Tank UG		20	20	13-Aug-26	10-Sep-26
STS1 1100	Install UG Mechanical Piping	20	20	13-Aug-26	10-Sep-26
STS1 1110	Install UG LSS	20	20	13-Aug-26	10-Sep-26
STS1 1120	Install UG Electrical	15	15	13-Aug-26	02-Sep-26
STS1 1130	Install UG Plumbing	10	10	13-Aug-26	26-Aug-26
Level 1		150	150	16-Jul-26	18-Feb-27
STS1 1000	Pile Install - ST	20	20	16-Jul-26	12-Aug-26
STS1 1010	FRP Pile Caps/Grade Beams	40	40	11-Sep-26	05-Nov-26
STS1 1020	Stone Subgrade	10	10	06-Nov-26	19-Nov-26
STS1 1070	FRP Slab on Grade - ST	15	15	20-Nov-26	14-Dec-26
STS1 1030	FRP Tank Mat Foundation	10	10	15-Dec-26	29-Dec-26
STS1 1040	FRP Interior Columns	10	10	30-Dec-26	13-Jan-27
STS1 1060	FRP Tank Slab	5	5	30-Dec-26	06-Jan-27
STS1 1050	FRP Tank Walls	5	5	07-Jan-27	13-Jan-27
STS1 1080	FRP Interior/Exterior Walls	15	15	14-Jan-27	04-Feb-27
STS1 1090	CMU Wall Infills	10	10	05-Feb-27	18-Feb-27
Level 2		55	55	14-Jan-27	02-Apr-27
STS2 1000	FRP Interior Columns and Beams	20	20	14-Jan-27	11-Feb-27
STS2 1010	FRP Elevated Slab	20	20	12-Feb-27	11-Mar-27
STS2 1030	FRP Shallow Tank Framing	5	5	12-Mar-27	18-Mar-27
STS2 1040	FRP Shallow Tank Walls and Slab	5	5	19-Mar-27	25-Mar-27
STS2 1020	CMU Wall Infills	5	5	29-Mar-27	02-Apr-27
Level 3		55	55	12-Mar-27	28-May-27
STS3 1000	FRP Interior Columns and Beams	20	20	12-Mar-27	09-Apr-27
STS3 1030	FRP Elevated Slab	15	15	12-Apr-27	30-Apr-27
STS3 1010	FRP Tank Walls and Skimmers	10	10	03-May-27	14-May-27
STS3 1020	CMU Wall Infills	10	10	17-May-27	28-May-27
Roof		65	65	03-May-27	02-Aug-27
STSR 1020	FRP Interior Columns and Beams	15	15	03-May-27	21-May-27
STSR 1030	FRP Elevated Slab (Excluding Shark Tank)	15	15	24-May-27	14-Jun-27
A4940	FRP Leave out area	5	5	27-Jul-27	02-Aug-27
INTERIOR - ST		200	200	01-Jun-27	10-Mar-28

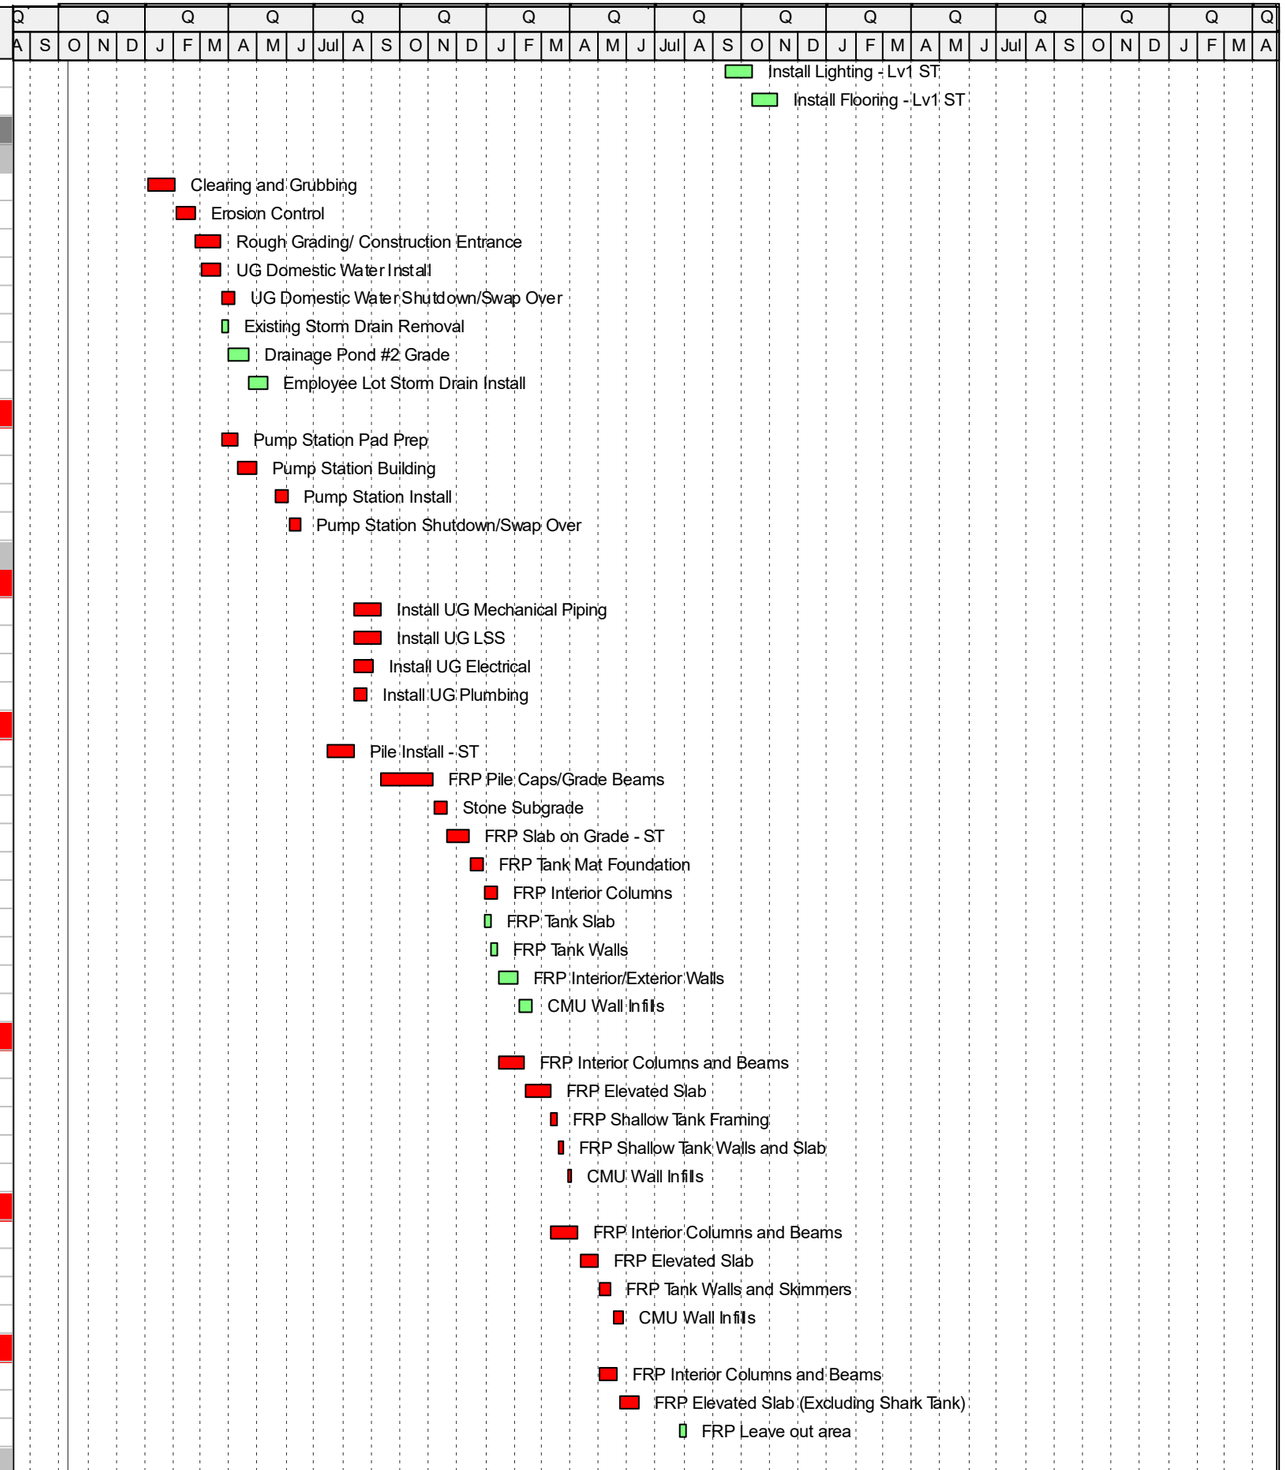

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

FF Aquarium Reno & Addition - BL 10.31.25

11-Oct-25

Remaining Work Schedule

CLANCY &THEYS CONSTRUCTION COMPANY

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
Level 1		170	170	15-Jun-27	11-Feb-28
Lv1 - Finishes		120	120	24-Aug-27	11-Feb-28
F1-510	Hang Drywall & Door Frames for MEP Rooms - Lv1 ST	10	10	24-Aug-27	07-Sep-27
F1-390	Hang Drywall Walls - Lv1 ST	15	15	31-Aug-27	21-Sep-27
F1-400	Tape & Finish Walls - Lv1 ST	20	20	22-Sep-27	19-Oct-27
F1-410	Hang Drywall Ceilings - Lv1 ST	5	5	06-Oct-27	12-Oct-27
F1-420	Tape & Finish Ceilings - Lv1 ST	5	5	13-Oct-27	19-Oct-27
F1-430	Prime Paint - Lv1 ST	10	10	20-Oct-27	02-Nov-27
F1-440	Install Ceiling Grid - Lv1 ST	15	15	03-Nov-27	23-Nov-27
F1-450	First Coat of Paint - Lv1 ST	15	15	03-Nov-27	23-Nov-27
F1-460	Install Door Frames - Lv1 ST	10	10	03-Nov-27	16-Nov-27
F1-470	Install Electrical Panels - Lv1 ST	20	20	03-Nov-27	02-Dec-27
F1-480	Install OH Mechanical Trim - Lv1 ST	20	20	24-Nov-27	23-Dec-27
F1-490	Install Lighting - Lv1 ST	20	20	24-Nov-27	23-Dec-27
F1-500	Install Flooring - Lv1 ST	20	20	24-Nov-27	23-Dec-27
F1-530	Seal Concrete Floor - Lv1 ST	5	5	24-Nov-27	02-Dec-27
F1-550	Install Bathroom Fixtures - Lv1 ST	10	10	24-Nov-27	09-Dec-27
F1-560	Install Sprinkler Drops & Heads - Lv1 ST	15	15	24-Nov-27	16-Dec-27
F1-570	Install Electrical Trim & Devices - Lv1 ST	15	15	03-Dec-27	23-Dec-27
F1-600	Install ACT - Lv1 ST	15	15	27-Dec-27	14-Jan-28
F1-610	Install Fixed Furniture - Lv1 ST	10	10	27-Dec-27	07-Jan-28
F1-620	Install Millwork - Lv1 ST	10	10	27-Dec-27	07-Jan-28
F1-1880	Final Coat of Paint - Lv1 ST	15	15	10-Jan-28	28-Jan-28
F1-590	Install Doors - Lv1 ST	10	10	31-Jan-28	11-Feb-28
Lv1 - Rough-in		80	80	15-Jun-27	05-Oct-27
R1-240	Layout & Framing - Lv1 ST	10	10	15-Jun-27	28-Jun-27
R1-250	Install Mechanical Rough - Lv1 ST	20	20	29-Jun-27	26-Jul-27
R1-340	Install OH LSS Rough - Lv1	30	30	29-Jun-27	09-Aug-27
R1-260	Install Electrical OH Rough - Lv1 ST	15	15	06-Jul-27	26-Jul-27
R1-270	Install Plumbing OH Rough - Lv1 ST	15	15	13-Jul-27	02-Aug-27
R1-280	Install Electrical In-Wall Rough - Lv1 ST	15	15	27-Jul-27	16-Aug-27
R1-290	Install Plumbing In-Wall Rough - Lv1 ST	10	10	03-Aug-27	16-Aug-27
R1-300	Install Sprinkler Rough - Lv1 ST	10	10	03-Aug-27	16-Aug-27
R1-350	Install Filters, Tanks & Pumps (LSS) -Lv1	30	30	10-Aug-27	21-Sep-27
R1-330	In-Wall Inspection - Lv1 ST	5	5	17-Aug-27	23-Aug-27
R1-310	Install Insulation - Lv1 ST	5	5	24-Aug-27	30-Aug-27
R1-320	OH MEP Inspection - Lv1 ST	5	5	22-Sep-27	28-Sep-27
R1-850	Install OH MEP Insulation - L1 S1	5	5	29-Sep-27	05-Oct-27
Level 2		170	170	29-Jun-27	25-Feb-28
Lv2 - Rough-in		55	55	29-Jun-27	14-Sep-27
R1-860	Layout & Framing - Lv2 ST	10	10	29-Jun-27	12-Jul-27
R1-880	Install Mechanical Rough - Lv2 ST	20	20	13-Jul-27	09-Aug-27
R1-1110	Install OH LSS Rough - Lv2	30	30	13-Jul-27	23-Aug-27
R1-890	Install Electrical OH Rough - Lv2 ST	15	15	20-Jul-27	09-Aug-27
R1-870	Install Plumbing OH Rough - Lv2 ST	15	15	27-Jul-27	16-Aug-27
R1-910	Install Electrical In-Wall Rough - Lv2 ST	15	15	10-Aug-27	30-Aug-27
R1-900	Install Plumbing In-Wall Rough - Lv2 ST	10	10	17-Aug-27	30-Aug-27
R1-920	Install Sprinkler Rough - Lv2 ST	10	10	17-Aug-27	30-Aug-27
R1-940	In-Wall Inspection - Lv2 ST	5	5	31-Aug-27	07-Sep-27
R1-950	OH MEP Inspection - Lv2 ST	5	5	31-Aug-27	07-Sep-27

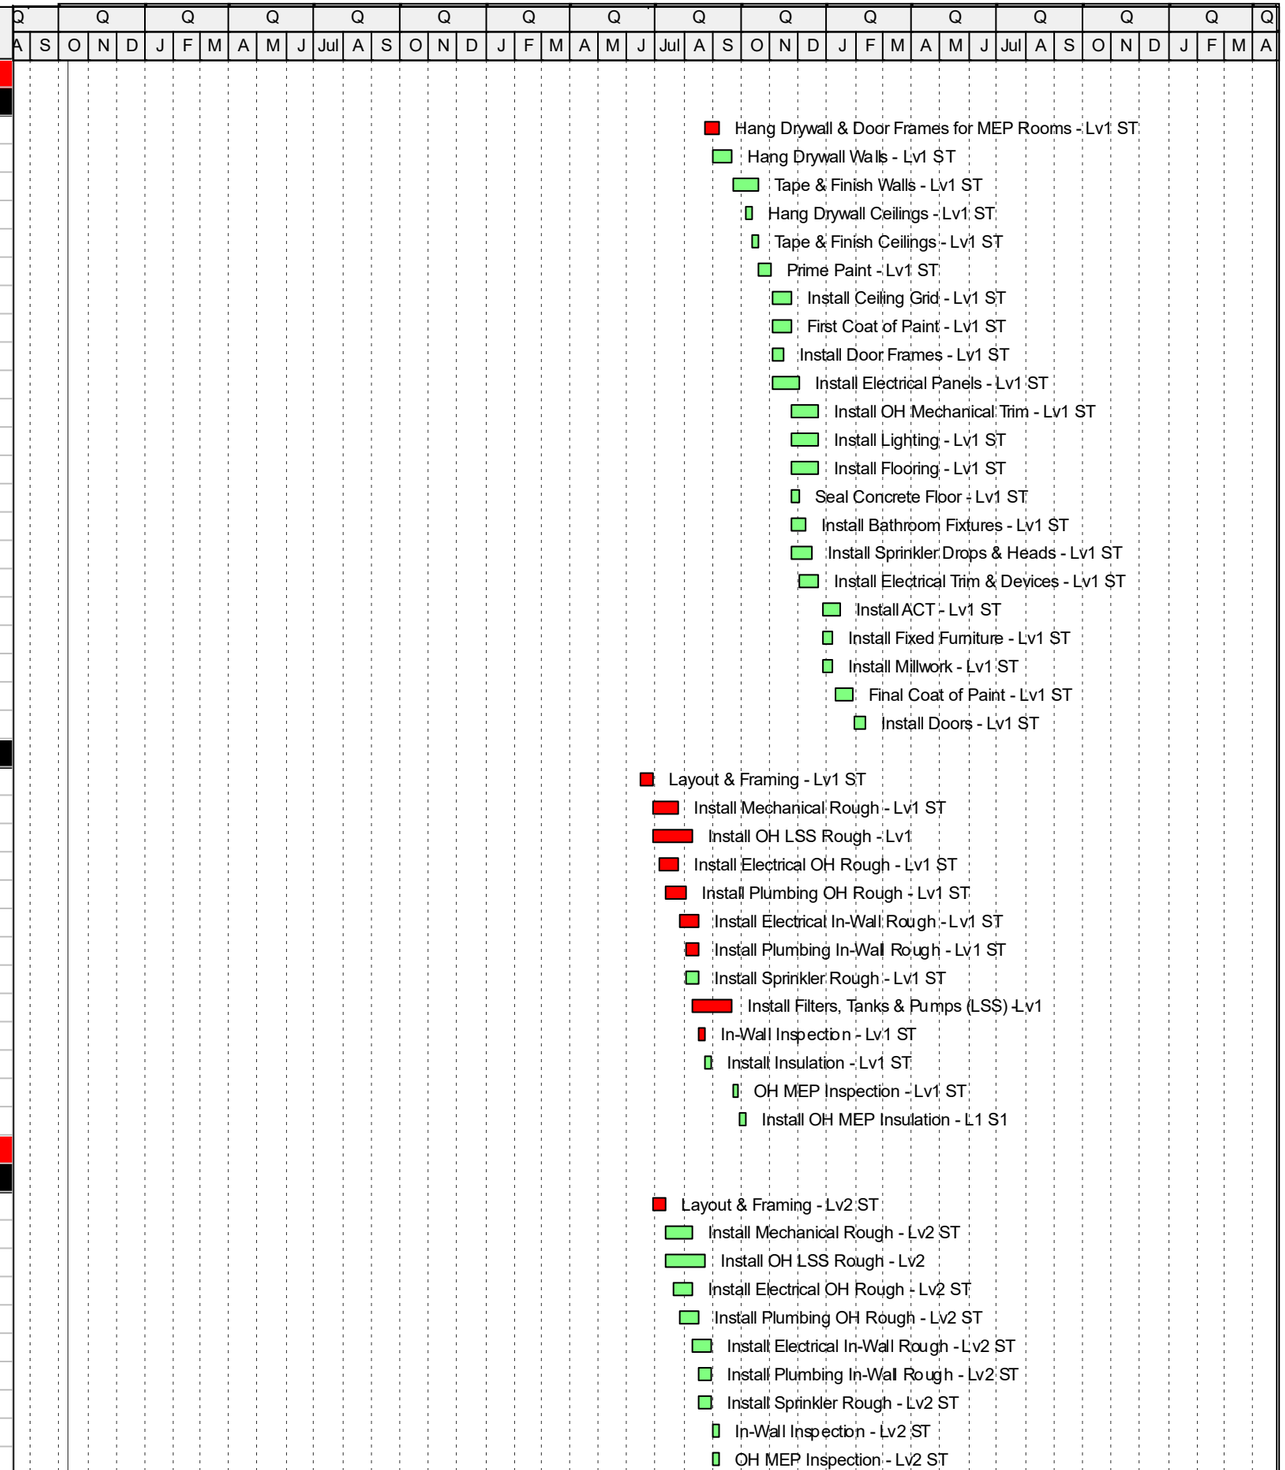

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

FF Aquarium Reno & Addition - BL 10.31.25

11-Oct-25
Remaining Work Schedule

CLANCY & THEYS CONSTRUCTION COMPANY

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
R1-930	Install Insulation - Lv2 ST	5	5	08-Sep-27	14-Sep-27
R1-960	Install OH MEP Insulation - L1 S1	5	5	08-Sep-27	14-Sep-27
Lv2 - Finishes		115	115	15-Sep-27	25-Feb-28
F1-1890	Hang Drywall Walls - Lv2 ST	15	15	15-Sep-27	05-Oct-27
F1-1900	Tape & Finish Walls - Lv2 ST	20	20	06-Oct-27	02-Nov-27
F1-2010	Hang Drywall Ceilings - Lv2 ST	5	5	06-Oct-27	12-Oct-27
F1-2020	Tape & Finish Ceilings - Lv2 ST	5	5	13-Oct-27	19-Oct-27
F1-1940	Prime Paint - Lv2 ST	10	10	03-Nov-27	16-Nov-27
F1-1910	Install Ceiling Grid - Lv2 ST	15	15	17-Nov-27	09-Dec-27
F1-1950	First Coat of Paint - Lv2 ST	15	15	17-Nov-27	09-Dec-27
F1-2030	Install Door Frames - Lv2 ST	10	10	17-Nov-27	02-Dec-27
F1-2100	Install Electrical Panels - Lv2 ST	20	20	17-Nov-27	16-Dec-27
F1-1920	Install OH Mechanical Trim - Lv2 ST	20	20	10-Dec-27	07-Jan-28
F1-1930	Install Lighting - Lv2 ST	20	20	10-Dec-27	07-Jan-28
F1-1960	Install Flooring - Lv2 ST	20	20	10-Dec-27	07-Jan-28
F1-1980	Seal Concrete Floor - Lv2 ST	5	5	10-Dec-27	16-Dec-27
F1-2000	Install Bathroom Fixtures - Lv2 ST	10	10	10-Dec-27	23-Dec-27
F1-2090	Install Sprinkler Drops & Heads - Lv2 ST	15	15	10-Dec-27	31-Dec-27
F1-2050	Install Electrical Trim & Devices - Lv2 ST	15	15	17-Dec-27	07-Jan-28
F1-2060	Install ACT - Lv2 ST	15	15	10-Jan-28	28-Jan-28
F1-2070	Install Fixed Furniture - Lv2 ST	10	10	10-Jan-28	21-Jan-28
F1-2080	Install Millwork - Lv2 ST	10	10	10-Jan-28	21-Jan-28
F1-2110	Final Coat of Paint - Lv2 ST	15	15	24-Jan-28	11-Feb-28
F1-2040	Install Doors - Lv2 ST	10	10	14-Feb-28	25-Feb-28
Level 3		170	170	13-Jul-27	10-Mar-28
Lv3 - Rough-in		55	55	13-Jul-27	28-Sep-27
R1-970	Layout & Framing - Lv3 ST	10	10	13-Jul-27	26-Jul-27
R1-990	Install Mechanical Rough - Lv3 ST	20	20	27-Jul-27	23-Aug-27
R1-1000	Install Electrical OH Rough - Lv3 ST	15	15	03-Aug-27	23-Aug-27
R1-980	Install Plumbing OH Rough - Lv3 ST	15	15	10-Aug-27	30-Aug-27
R1-1020	Install Electrical In-Wall Rough - Lv3 ST	15	15	24-Aug-27	14-Sep-27
R1-1010	Install Plumbing In-Wall Rough - Lv3 ST	10	10	31-Aug-27	14-Sep-27
R1-1030	Install Sprinkler Rough - Lv3 ST	10	10	31-Aug-27	14-Sep-27
R1-1050	In-Wall Inspection - Lv3 ST	5	5	15-Sep-27	21-Sep-27
R1-1060	OH MEP Inspection - Lv3 ST	5	5	15-Sep-27	21-Sep-27
R1-1040	Install Insulation - Lv3 ST	5	5	22-Sep-27	28-Sep-27
R1-1070	Install OH MEP Insulation - L1 S1	5	5	22-Sep-27	28-Sep-27
Lv3 - Finishes		115	115	29-Sep-27	10-Mar-28
F1-2120	Hang Drywall Walls - Lv3 ST	15	15	29-Sep-27	19-Oct-27
F1-2130	Tape & Finish Walls - Lv3 ST	20	20	20-Oct-27	16-Nov-27
F1-2240	Hang Drywall Ceilings - Lv3 ST	5	5	20-Oct-27	26-Oct-27
F1-2250	Tape & Finish Ceilings - Lv3 ST	5	5	27-Oct-27	02-Nov-27
F1-2170	Prime Paint - Lv3 ST	10	10	17-Nov-27	02-Dec-27
F1-2140	Install Ceiling Grid - Lv3 ST	15	15	03-Dec-27	23-Dec-27
F1-2180	First Coat of Paint - Lv3 ST	15	15	03-Dec-27	23-Dec-27
F1-2260	Install Door Frames - Lv3 ST	10	10	03-Dec-27	16-Dec-27
F1-2330	Install Electrical Panels - Lv3 ST	20	20	03-Dec-27	31-Dec-27
F1-2150	Install OH Mechanical Trim - Lv3 ST	20	20	27-Dec-27	21-Jan-28
F1-2160	Install Lighting - Lv3 ST	20	20	27-Dec-27	21-Jan-28
F1-2190	Install Flooring - Lv3 ST	20	20	27-Dec-27	21-Jan-28

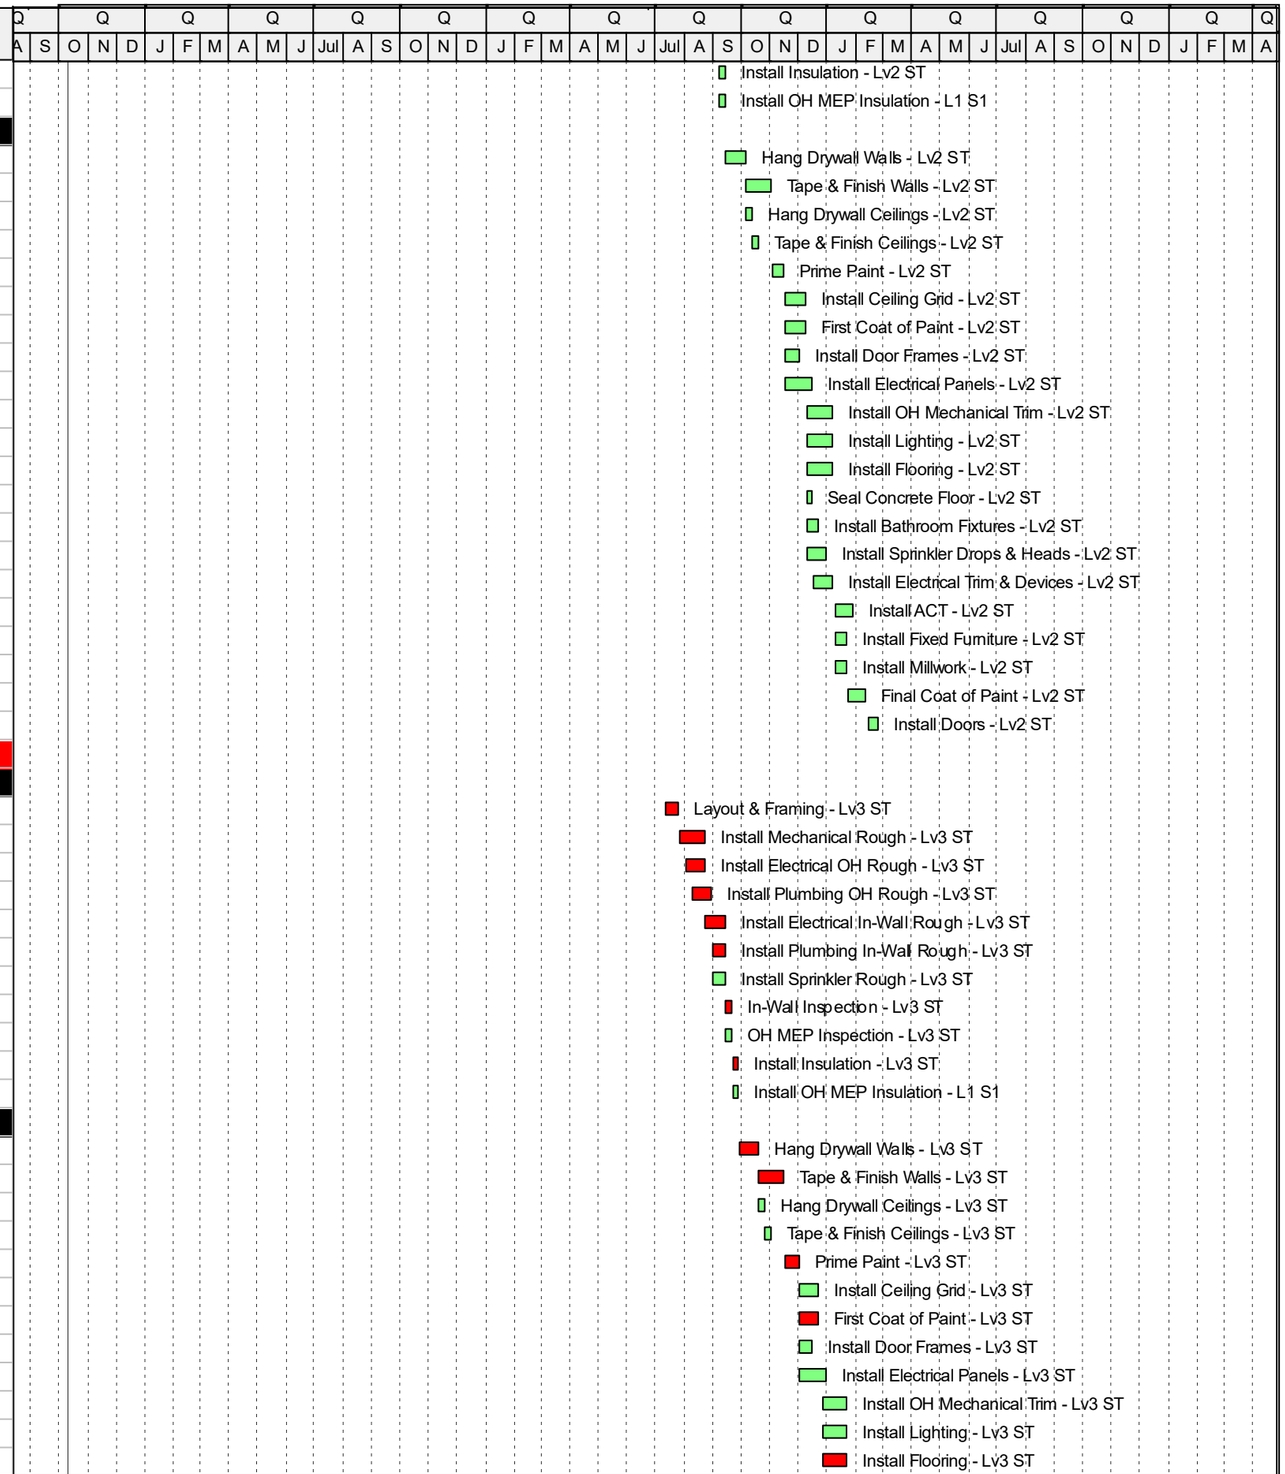

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

FF Aquarium Reno & Addition - BL 10.31.25

11-Oct-25
Remaining Work Schedule

CLANCY & THEYS CONSTRUCTION COMPANY

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
F1-2210	Seal Concrete Floor - Lv3 ST	5	5	27-Dec-27	31-Dec-27
F1-2230	Install Bathroom Fixtures - Lv3 ST	10	10	27-Dec-27	07-Jan-28
F1-2320	Install Sprinkler Drops & Heads - Lv3 ST	15	15	27-Dec-27	14-Jan-28
F1-2280	Install Electrical Trim & Devices - Lv3 ST	15	15	03-Jan-28	21-Jan-28
F1-2290	Install ACT - Lv3 ST	15	15	24-Jan-28	11-Feb-28
F1-2300	Install Fixed Furniture - Lv3 ST	10	10	24-Jan-28	04-Feb-28
F1-2310	Install Millwork - Lv3 ST	10	10	24-Jan-28	04-Feb-28
F1-2340	Final Coat of Paint - Lv3 ST	15	15	07-Feb-28	25-Feb-28
F1-2270	Install Doors - Lv3 ST	10	10	28-Feb-28	10-Mar-28
Shark Tank		150	150	01-Jun-27	31-Dec-27
STBG 1020	Inspect Concrete Tank	5	5	01-Jun-27	07-Jun-27
STBG 1030	Inspect Acrylic at Manufacturers Shop	5	5	01-Jun-27	07-Jun-27
STBG 1010	Sandblast Concrete	10	10	08-Jun-27	21-Jun-27
STBG 1040	Apply Waterproofing	20	20	22-Jun-27	19-Jul-27
STBG 1050	Ship Acryic to Site	10	10	06-Jul-27	19-Jul-27
STBG 1060	Install Acrylic with Crane (Rigging Company)	5	5	20-Jul-27	26-Jul-27
STBG 1070	Install Silicone	15	15	27-Jul-27	16-Aug-27
STBG 1080	Cure Silicone	20	20	17-Aug-27	14-Sep-27
STBG 1090	Hydrotest	25	25	15-Sep-27	19-Oct-27
STBG 1100	Witness Hydrotest	2	2	22-Sep-27	23-Sep-27
STBG 1110	Drain Tank	5	5	20-Oct-27	26-Oct-27
STBG 1120	Install Acrylic Protection Panels	15	15	27-Oct-27	16-Nov-27
STBG 1130	Install LSS	10	10	17-Nov-27	02-Dec-27
STBG 1150	Install Exhibits	25	25	17-Nov-27	23-Dec-27
STBG 1140	Commission LSS	20	20	03-Dec-27	31-Dec-27
FACADE & ROOFING - ST		30	30	15-Jun-27	26-Jul-27
A4130	Install Roofing - ST	30	30	15-Jun-27	26-Jul-27
RENOVATION		430	430	05-Jan-26	14-Sep-27
DEMO - RN		80	80	05-Jan-26	28-Apr-26
A4140	Shutdowns & Selective Demo	80	80	05-Jan-26	28-Apr-26
A4150	Investigate MEP Demo	25	25	05-Jan-26	09-Feb-26
SUPERSTRUCTURE - RN		175	175	18-Jun-26	25-Feb-27
STS1 1140	Pile Install - RN	20	20	18-Jun-26	15-Jul-26
STS1 1150	FRP Pile Caps/Grade Beams	40	40	09-Oct-26	07-Dec-26
STS1 1160	Subgrade	10	10	08-Dec-26	21-Dec-26
STS1 1170	FRP Slab on Grade	15	15	22-Dec-26	13-Jan-27
STS1 1180	FRP Vertical Walls (Touch Tank) - RN	15	15	14-Jan-27	04-Feb-27
STS1 1190	FRP Lv2 Slab - RN	15	15	05-Feb-27	25-Feb-27
INTERIOR - RN		170	170	14-Jan-27	14-Sep-27
Level 1		170	170	14-Jan-27	14-Sep-27
Lv1 - Rough-in		55	55	14-Jan-27	02-Apr-27
R1-1120	Layout & Framing - Lv1 RN	10	10	14-Jan-27	28-Jan-27
R1-1140	Install Mechanical Rough - Lv1 RN	20	20	29-Jan-27	25-Feb-27
R1-1150	Install Electrical OH Rough - Lv1 RN	15	15	05-Feb-27	25-Feb-27
R1-1130	Install Plumbing OH Rough - Lv1 RN	15	15	12-Feb-27	04-Mar-27
R1-1170	Install Electrical In-Wall Rough - Lv1 RN	15	15	26-Feb-27	18-Mar-27
R1-1160	Install Plumbing In-Wall Rough - Lv1 RN	10	10	05-Mar-27	18-Mar-27
R1-1180	Install Sprinkler Rough - Lv1 RN	10	10	05-Mar-27	18-Mar-27
R1-1200	In-Wall Inspection - Lv1 RN	5	5	19-Mar-27	25-Mar-27
R1-1210	OH MEP Inspection - Lv1 RN	5	5	19-Mar-27	25-Mar-27

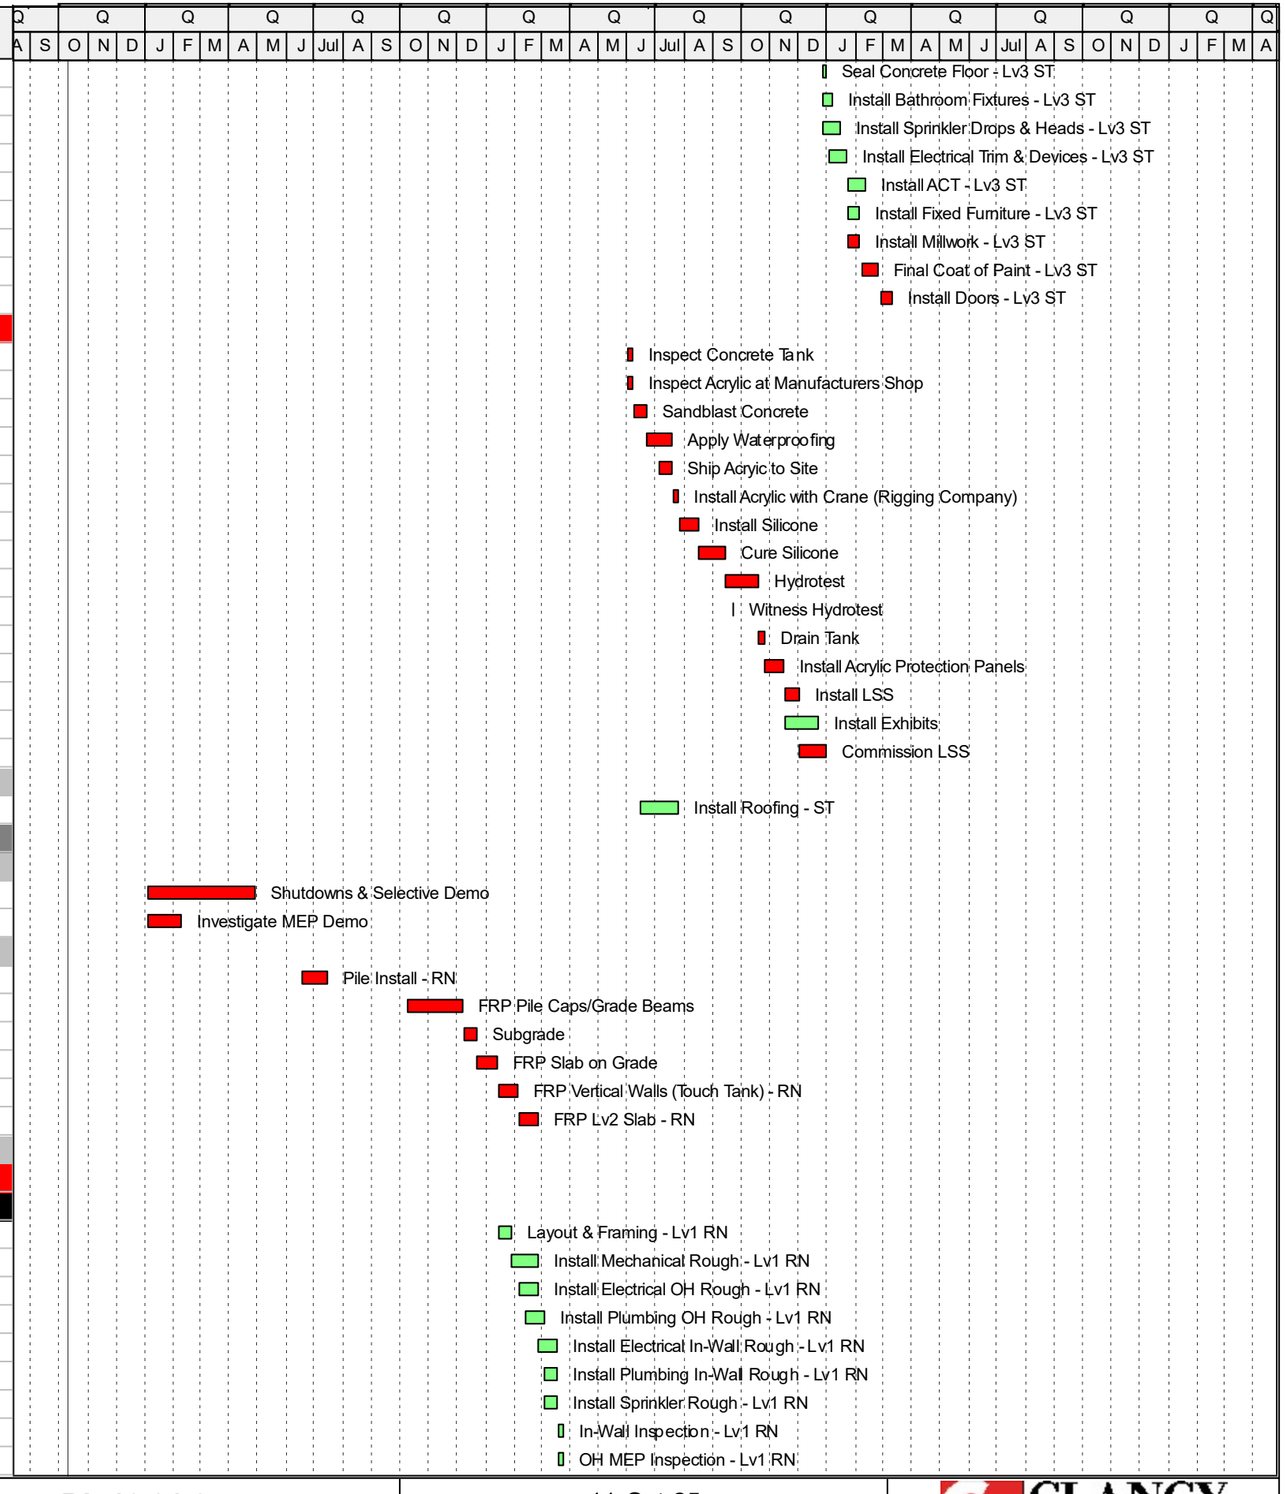

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

FF Aquarium Reno & Addition - BL 10.31.25

11-Oct-25

Remaining Work Schedule

CLANCY & THEYS CONSTRUCTION COMPANY

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
R1-1190	Install Insulation - Lv1 RN	5	5	29-Mar-27	02-Apr-27
R1-1220	Install OH MEP Insulation - Lv1 RN	5		29-Mar-27	02-Apr-27
Lv1 - Finishes		160	160	29-Jan-27	14-Sep-27
F1-2630	Install Exterior Doors - Lv1 RN	10	10	29-Jan-27	11-Feb-27
F1-2620	Install Storefront - Lv1 RN	15	15	12-Feb-27	04-Mar-27
F1-2400	Hang Drywall Walls - Lv1 RN	15	15	05-Apr-27	23-Apr-27
F1-2410	Tape & Finish Walls - Lv1 RN	20	20	26-Apr-27	21-May-27
F1-2500	Hang Drywall Ceilings - Lv1 RN	5	5	26-Apr-27	30-Apr-27
F1-2510	Tape & Finish Ceilings - Lv1 RN	5	5	03-May-27	07-May-27
F1-2450	Prime Paint - Lv1 RN	10	10	24-May-27	07-Jun-27
F1-2420	Install Ceiling Grid - Lv1 RN	15	15	08-Jun-27	28-Jun-27
F1-2460	First Coat of Paint - Lv1 RN	15	15	08-Jun-27	28-Jun-27
F1-2520	Install Door Frames - Lv1 RN	10	10	08-Jun-27	21-Jun-27
F1-2590	Install Electrical Panels - Lv1 RN	20	20	08-Jun-27	05-Jul-27
F1-2430	Install OH Mechanical Trim - Lv1 RN	20	20	29-Jun-27	26-Jul-27
F1-2440	Install Lighting - Lv1 RN	20	20	29-Jun-27	26-Jul-27
F1-2470	Install Flooring - Lv1 RN	20	20	29-Jun-27	26-Jul-27
F1-2480	Seal Concrete Floor - Lv1 RN	5	5	29-Jun-27	05-Jul-27
F1-2490	Install Bathroom Fixtures - Lv1 RN	10	10	29-Jun-27	12-Jul-27
F1-2580	Install Sprinkler Drops & Heads - Lv1 RN	15	15	29-Jun-27	19-Jul-27
F1-2610	Apply Acoustic Spray Ceiliongs - Lv1 RN	10	10	29-Jun-27	12-Jul-27
F1-2540	Install Electrical Trim & Devices - Lv1 RN	15	15	06-Jul-27	26-Jul-27
F1-2550	Install ACT - Lv1 RN	15	15	27-Jul-27	16-Aug-27
F1-2560	Install Fixed Furniture - Lv1 RN	10	10	27-Jul-27	09-Aug-27
F1-2570	Install Millwork - Lv1 RN	10	10	27-Jul-27	09-Aug-27
F1-2600	Final Coat of Paint - Lv1 RN	15	15	10-Aug-27	30-Aug-27
F1-2530	Install Doors - Lv1 RN	10	10	31-Aug-27	14-Sep-27
Lv1 - Bathrooms		70	70	19-Mar-27	28-Jun-27
A4320	Install MEP Rough in - Lv1 Br	20	20	19-Mar-27	16-Apr-27
A4370	Close Walls & Finish - Lv1 Br	10	10	19-Apr-27	30-Apr-27
A4360	Install Bathroom Tile - Lv1 Br	10	10	03-May-27	14-May-27
A4350	Install MEP Trim - Lv1 Br	10	10	17-May-27	28-May-27
A4330	Install Countertops - Lv1 Br	10	10	01-Jun-27	14-Jun-27
A4340	Install Bathroom Fixtures and Partitions - Lv1 Br	10	10	15-Jun-27	28-Jun-27
Level 2		122	122	26-Feb-27	18-Aug-27
Lv2 - Rough-in		50	50	26-Feb-27	07-May-27
R1-1230	Layout & Framing - Lv2 RN	10	10	26-Feb-27	11-Mar-27
R1-1250	Install Mechanical Rough - Lv2 RN	12	12	12-Mar-27	30-Mar-27
F1-2860	Install FRP Tanks - Lv2 RN	15	15	12-Mar-27	02-Apr-27
R1-1260	Install Electrical OH Rough - Lv2 RN	10	10	19-Mar-27	02-Apr-27
R1-1240	Install Plumbing OH Rough - Lv2 RN	10	10	29-Mar-27	09-Apr-27
R1-1280	Install Electrical In-Wall Rough - Lv2 RN	10	10	05-Apr-27	16-Apr-27
R1-1270	Install Plumbing In-Wall Rough - Lv2 RN	10	10	12-Apr-27	23-Apr-27
R1-1290	Install Sprinkler Rough - Lv2 RN	10	10	12-Apr-27	23-Apr-27
R1-1310	In-Wall Inspection - Lv2 RN	5	5	26-Apr-27	30-Apr-27
R1-1320	OH MEP Inspection - Lv2 RN	5	5	26-Apr-27	30-Apr-27
R1-1300	Install Insulation - Lv2 RN	5	5	03-May-27	07-May-27
R1-1330	Install OH MEP Insulation - Lv2 RN	5	5	03-May-27	07-May-27
Lv2 - Finishes		72	72	10-May-27	18-Aug-27
F1-2640	Hang Drywall Walls - Lv2 RN	10	10	10-May-27	21-May-27

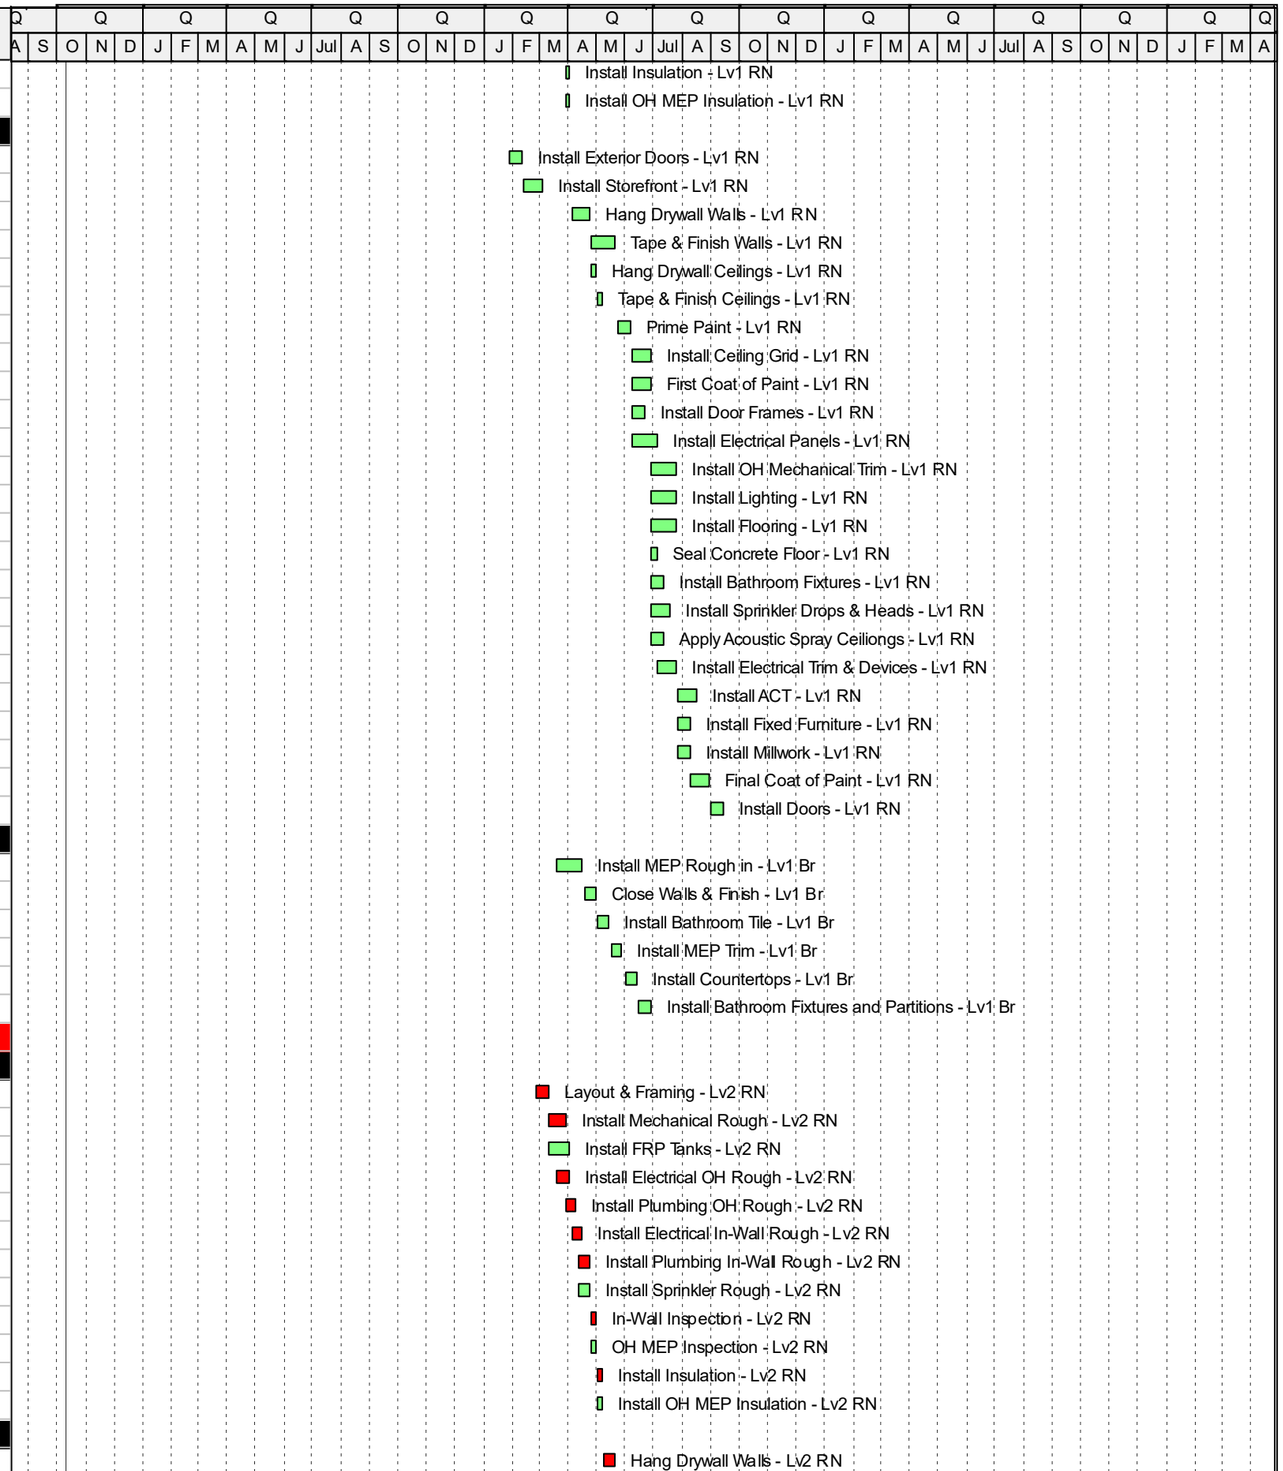

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

FF Aquarium Reno & Addition - BL 10.31.25

11-Oct-25
Remaining Work Schedule

CLANCY & THEYS CONSTRUCTION COMPANY

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
F1-2650	Tape & Finish Walls - Lv2 RN	12	12	24-May-27	09-Jun-27
F1-2740	Hang Drywall Ceilings - Lv2 RN	5	5	24-May-27	28-May-27
F1-2750	Tape & Finish Ceilings - Lv2 RN	5	5	01-Jun-27	07-Jun-27
F1-2690	Prime Paint - Lv2 RN	7	7	10-Jun-27	18-Jun-27
F1-2660	Install Ceiling Grid - Lv2 RN	7	7	21-Jun-27	29-Jun-27
F1-2700	First Coat of Paint - Lv2 RN	7	7	21-Jun-27	29-Jun-27
F1-2760	Install Door Frames - Lv2 RN	5	5	21-Jun-27	25-Jun-27
F1-2830	Install Electrical Panels - Lv2 RN	12	12	21-Jun-27	06-Jul-27
F1-2670	Install OH Mechanical Trim - Lv2 RN	12	12	30-Jun-27	15-Jul-27
F1-2680	Install Lighting - Lv2 RN	12	12	30-Jun-27	15-Jul-27
F1-2710	Install Flooring - Lv2 RN	12	12	30-Jun-27	15-Jul-27
F1-2720	Seal Concrete Floor - Lv2 RN	5	5	30-Jun-27	06-Jul-27
F1-2730	Install Bathroom Fixtures - Lv2 RN	7	7	30-Jun-27	08-Jul-27
F1-2820	Install Sprinkler Drops & Heads - Lv2 RN	10	10	30-Jun-27	13-Jul-27
F1-2850	Apply Acoustic Spray Ceilings - Lv2 RN	7	7	30-Jun-27	08-Jul-27
F1-2780	Install Electrical Trim & Devices - Lv2 RN	10	10	07-Jul-27	20-Jul-27
F1-2790	Install ACT - Lv2 RN	10	10	16-Jul-27	29-Jul-27
F1-2800	Install Fixed Furniture - Lv2 RN	7	7	16-Jul-27	26-Jul-27
F1-2810	Install Millwork - Lv2 RN	7	7	16-Jul-27	26-Jul-27
F1-2840	Final Coat of Paint - Lv2 RN	10	10	27-Jul-27	09-Aug-27
F1-2770	Install Doors - Lv2 RN	7	7	10-Aug-27	18-Aug-27
Lv2 - Bathrooms		35	35	26-Apr-27	14-Jun-27
A4380	Install MEP Rough in - Lv2 Br	10	10	26-Apr-27	07-May-27
A4430	Close Walls & Finish - Lv2 Br	5	5	10-May-27	14-May-27
A4420	Install Bathroom Tile - Lv2 Br	5	5	17-May-27	21-May-27
A4410	Install MEP Trim - Lv2 Br	5	5	24-May-27	28-May-27
A4390	Install Countertops - Lv2 Br	5	5	01-Jun-27	07-Jun-27
A4400	Install Bathroom Fixtures and Partitions - Lv2 Br	5	5	08-Jun-27	14-Jun-27
MEP EQUIPMENT		100	100	08-Sep-27	28-Jan-28
A4310	Service Inspection	5	5	08-Sep-27	14-Sep-27
A4300	Energize New Panels	20	20	15-Sep-27	12-Oct-27
R1-1340	Install LSS Equipment / Piping - Lv2 RN	20	20	22-Sep-27	19-Oct-27
A4170	Place & Fitout Chiller Platform	30	30	13-Oct-27	23-Nov-27
A4280	Energize Mechanical Equipment	20	20	13-Oct-27	09-Nov-27
A4180	Connect and Energize Chillers	20	20	24-Nov-27	23-Dec-27
A4190	Set & Connect Fuel Tank	20	20	24-Nov-27	23-Dec-27
A4200	Connect & Energize Generator	20	20	24-Nov-27	23-Dec-27
A4290	Energize LSS Equipment	20	20	03-Jan-28	28-Jan-28
SITE IMPROVEMENTS		435	435	22-Apr-26	07-Jan-28
CI1000	Install Storm Water	80	80	22-Apr-26	12-Aug-26
CI1040	Demo Existing Entrance	20	20	13-Aug-26	10-Sep-26
CI1010	Paving/Sidewalks	30	30	11-Sep-26	22-Oct-26
CI1030	Install Sculptures	20	20	23-Oct-26	19-Nov-26
CI1020	Landscaping	20	20	10-Dec-27	07-Jan-28
CLOSEOUT		141	141	10-Dec-27	26-Jun-28
CT Commissioning		55	55	10-Dec-27	25-Feb-28
CX1000	Commissioning	55	55	10-Dec-27*	25-Feb-28
Aquatic Commissioning		86	86	28-Feb-28	26-Jun-28
AX1000	Aquatic Commissioning	86	86	28-Feb-28	26-Jun-28

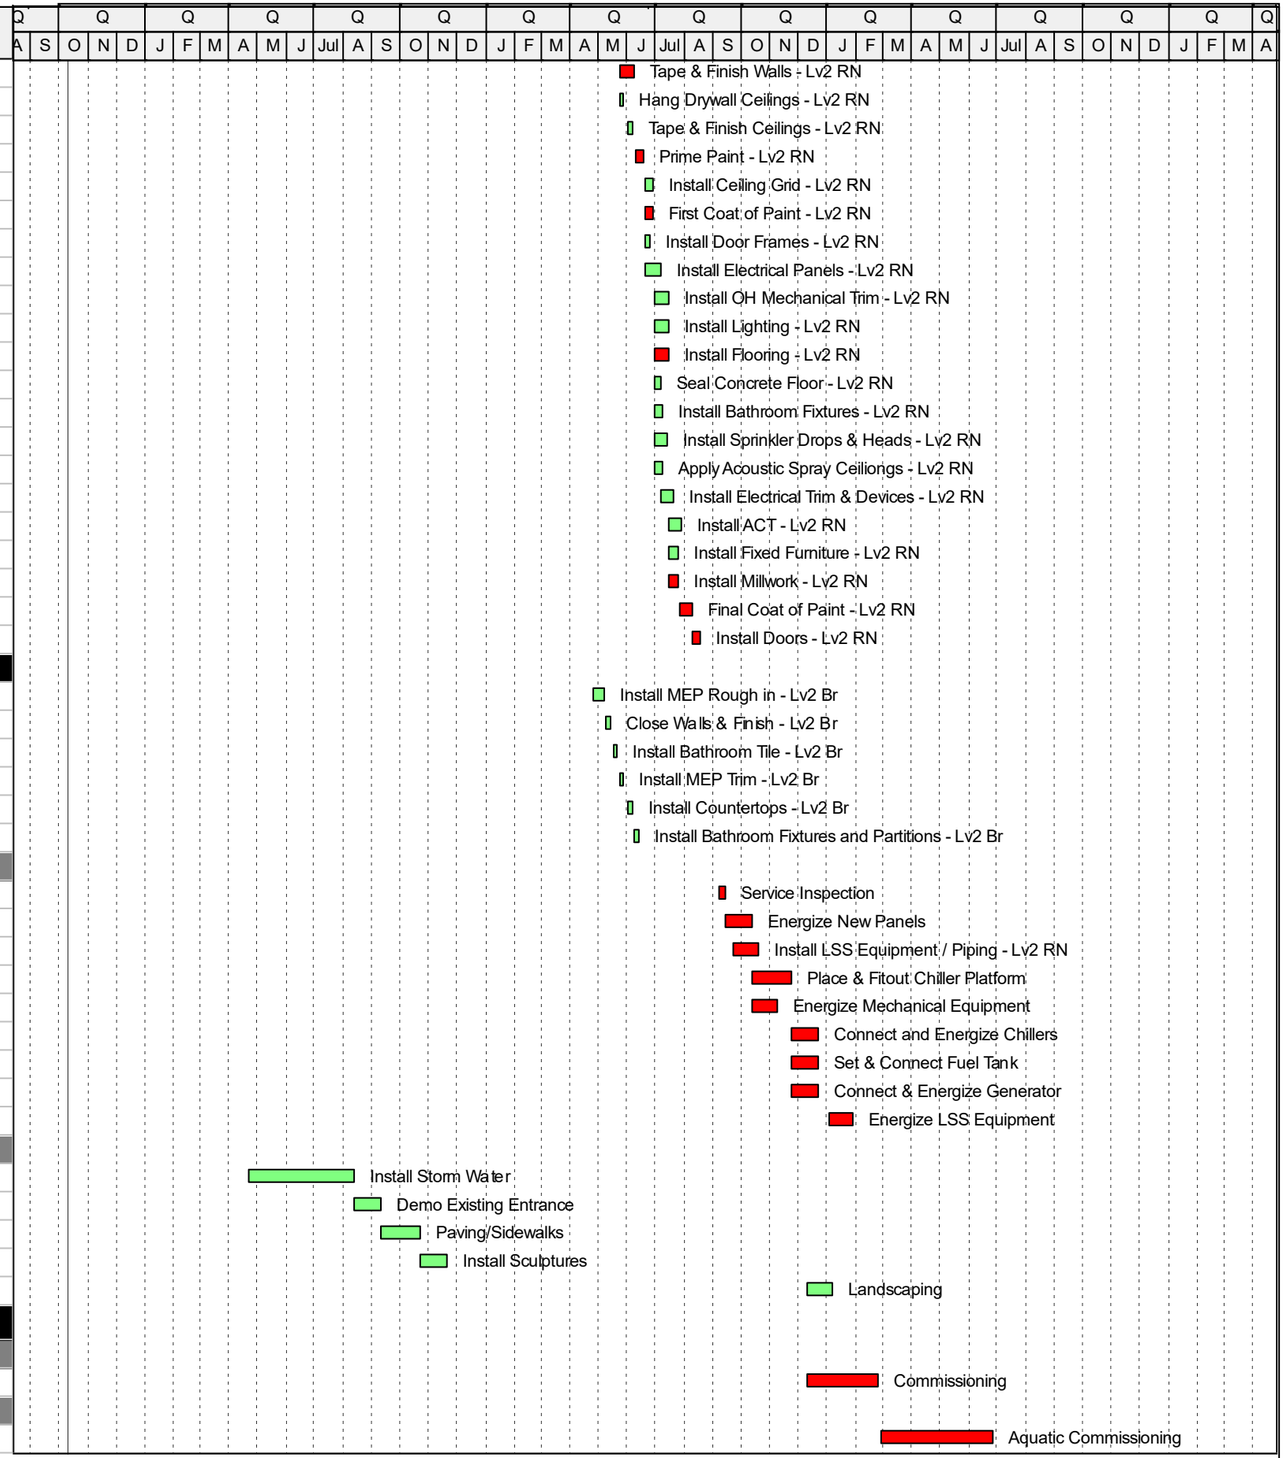

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

FF Aquarium Reno & Addition - BL 10.31.25

11-Oct-25

Remaining Work Schedule

CLANCY & THEYS CONSTRUCTION COMPANY
