Addendum #1



Project: Pamlico County School 6-12,

601 Main Street Bayboro, NC 28515 Pamlico County, NC

Owner: Pamlico County Schools

507 Anderson Dr. Bayboro, NC 28515

Architect: SfL+a Architects CM at Risk: Metcon, Inc.

333 Fayetteville Street, Suite 225, 763 Comtech Drive Raleigh, NC 27601 Pembroke, NC 28372

Date: July 12, 2024.

Notice to all: The following modifications, additions, deletions, clarifications, and/or information are hereby made part of the Contract Documents and shall be fully binding. The addendum must be acknowledged as part of the Bid Form.

Item #1: RFI Log:

A. Please see the attached RFI log as of 07/12/2024. (4 pages)

Item #2: Prebid Presentation

Item #3: Prebid Sign in Sheets

- A. Online chat sign in sheet (14 Pages)
- B. In person sign in sheet (1 Page)

END OF ADDENDUM #1

metcon **Pamlico County School 6-12** REQUEST REQUEST LOCATION **ANSWER QUESTION** RESPONSE RESPONDER TRADE/SCOPE **REQUEST BY** DATE Plans/Spec/Bid DATE ITEM# Scope of work states to include Commercial Laundry Equipment and Residential Equipment. Is there drawings and There will be no schedule provided. See Spec Section 11 21 6/25/2024 Plans SFLA 7/2/2024 BP1140 Singer Equipment equipment schedules with indicating these items and the quantities? 73.10 for Commercial Laundry Equpment. BOD is provided. Reviewing the scope of work for BP1140, I see it calls for this bid package to be responsible for the 11 27 73.10 Commercial No, the 11 27 73 (Commercial laundry spec section) and the 11 30 2 6/26/2024 13 (residential equipment) will not be moved to BP0150 General Metcon RP1140 11400 - Food Service Scope laundry spec section, and the 11 30 13 residential spec section. We are not a laundry or a residential equipment dealer, and Trades Scope. both fall outside of our wheelhouse of work. Can these spec sections be moved to the BP0150 general trades scope? Line 32 in the BP1140 scope of work states that this scope of work is responsible for final connections. Final connections are | Electrical contractor will bring power to the location of the 6/26/2024 Scope clearly indicated by MEP trades in the other scopes of work and on E-501, P-408, and FS Drawings. Please confirm final appliance, each subcontractor is responsible for making their final Metcon BP1140 11400 - Food Service electrical connection at the appliance. connections are by others. Line 33 in the BP1140 scope of work states that this scope of work is responsible for kitchen exhaust fans, and make-up air MC is responsible for the hood, exhaust and make-up air units for the units. These are indicated in the 11 40 00 specs as by mechanical (page 1) and listed on M-003 as by the MC. M-003 also kitchen. Fire Suppression Contractor will be responsible for the hood fire 6/26/2024 Scope indicates that the MC is responsible for the hood, fire suppression system, and fans. Please confirm that the MC is Metcon BP1140 11400 - Food Service suppression system. (line 33 on the Food service equipment Scope will responsible for the exhaust and make-up air units for the kitchen. Also please verify who is responsible for providing and be deleted and added to the Mechanical Scope) installing the hood and fire suppression system. Spec 123553.19 calls for white oak and red oak in the spec. Which veneer is desired? Red oak is a standard veneer 6/26/2024 Specifications Red Oak, Specification to be revised. SFLA 6/27/2024 BP1230 Nycom while white oak will be much more costly. Spec 123553.19 calls for the back of doors and interiors of the cabinets to be stained. Please confirm this is required 6/26/2024 Specifications This is required. SFLA 6/28/2024 BP1230 Nycom and the added cost should be included. Specifications will be revised. Sign Schedule is not provided. Refer to drawings for all sign locations. We will issues revision to the Section 101400 Signage - 2.3 Room Identification Signs 15. C. "Refer to Signage Schedule". Please provide a "Signage | documents to include additional general notes for signage. Note 6/26/2024 SFLA 7/2/2024 **Drawings** BP1014 **AOA Signs** Schedule" correlating with the signage elevations detailed on 1/A-520. will include but not be limited to "Provide Signage at all interior door locations. Rooms with more than one access point shall require signage at each location." Section 101400 Signage - 2.6 Dimensional Letter Signs C. 6. Copy List does NOT include Copy: "Pamlico County Middle 6/26/2024 **Drawings** School" (5/A-423) This is required. Specifications to be revised. SFLA 7/2/2024 BP1014 **AOA Signs** Please confirm the copy "Pamlico County Middle School" detailed on drawing A-423 is required. Line 11 of the carpet/resilient scope BP0960 under trade specific section notes that resilient athletic flooring to be provided by this contractor The Athletic flooring scope sheet BP0964, however, lists the resilient athletic flooring spec section as being included in Resilient athletic flooring belongs in the wood athletic flooring scope. 6/26/2024 Scope Metcon BP0960 Bonitz (Remove line 11 of BP0960) this package with the wood athletic flooring. Does the resilient athletic flooring belong in the carpet/resilient scope, or with the wood athletic flooring scope? There will be 2 employee parking areas that will have extra conex laydown area. In addition to that there will be more storage and lay 10 6/27/2024 Logistics Will there be any additional layout areas available for Conex's/ storage? Describe logistics for employee parking? Metcon 6/27/2024 BP0150 Pre-Bid down area by the job site trailer and towards the back of the new building. Please refer to the logistics plan. No, ground improvement will only be used around the foundations 6/27/2024 6/27/2024 BP1073/3160 11 Drawings/Scope Regarding the canopy foundations , Will you need this supported by the ground improvement (aggregate pier scope)? Metcon Pre-Bid Subcontractor will have to fill out prequalification forms A and B. 12 6/27/2024 Bid Manual and go through the review process. Please call Ms. Tina for more Metcon 6/27/2024 Pre-Bid What is the process for becoming a pre-qualified tier 1 subcontractor for this project?

METCON RFI LOG Page: 1 of 4

Duct cleaning will be required per the spec.

Metcon

6/27/2024

BP2300

Pre-Bid

13

6/27/2024

Specifications

Will duct cleaning be required per spec or only if it fails cleanliness test?

Damling County School 6 12



Pamlico County School 6-12								
ITEM#	REQUEST DATE	REQUEST LOCATION Plans/Spec/Bid Manual	QUESTION	RESPONSE	RESPONDER	ANSWER DATE	TRADE/SCOPE	REQUEST BY
14	6/27/2024	Wantial	Who will be setting Trimble points, will they be in each room as needed?	Tremble points will not be set in each room. Control points at strategic points around the building will be set by Construction Manager to be used by subcontractors for doing their own layout.	Metcon	6/27/2024		Pre-Bid
15	6/27/2024	Bid Manual	Is there a preliminary phased construction schedule at this time?	Not at this time, a preliminary schedule will be provided in an upcoming addendum.	Metcon	6/27/2024		Pre-Bid
16	6/27/2024	ВІМ	Have you made a decision regarding BIM? Will sprinkler and cable tray be involved?	The sprinkler subcontractor will provide their own design and 3D drawings done with Auto desk, Revit or Navisworks. The completed sprinkler design will be used for coordination by the BIM Manager. Please refer to Bid package #2100 for fees associated with BIM coordination. Note, the BIM coordination allowance is not to be used against the subcontractor's time to build their 3D model. The BIM allowance is set to pay for the coordination done by the BIM Manager.	Metcon	6/27/2024		Pre-Bid
17	6/27/2024	Drawings	Regarding the structural details, most connections show flag bars, can alternate details be provided to lower the cost for welding?	Architect states this could be possible. Question to be sent as an RFI for further discussion with the Structural Engineer. A substitution request form will need to be submitted.	Metcon	6/27/2024		Pre-Bid
18	6/27/2024	Logistics	Please provide an equipment and crane access plan around the footprint of the new school, will there be access between the existing school and the new construction?	There will be crane and equipment access all around the building with the exception of a small area in the north-east, were the old building and the new building are closer together. Subcontractor will have to plan accordingly to complete their scope of work. Geotech reports will be made available for subcontractors to use while doing the crane pad and lift plan.	Metcon	6/27/2024		Pre-Bid
19	6/27/2024	BIM	If Metcon does the BIM, does the \$35,000 allowance need to be included in the cost?	Pre-coordination has been done, but full coordination will occur when all shop drawings are incorporated into the BIM model. If your scope of work calls for a BIM allowance, then it needs to be included in the bid	Metcon	6/27/2024		Pre-Bid
20	6/27/2024	Scope	Is there any additional information that can be provided for the photovoltaic alternate scope of work will be included in the build? Client interest?	As any alternate, after all the bids come in, the owner reserves the right to choose alternates at their discretion.	Metcon	6/27/2024		Pre-Bid
21	6/27/2024	Scope	Are the current bid packages amendable? There are items within Div. 10 package that traditionally fall under other scopes i.e lab equipment and ark kilns. Typically, we see visual displays and metal storage solutions within the specialties however they are separate on this project.	The scopes of work can be amendable depending on the situation and subcontractor feedback. There are no visual displays in this project and the kilns are owner provided.	Metcon	6/27/2024	BP1020	Pre-Bid
22	6/27/2024		Would proven clearance for entire crews to be able to work on military installations (DBIDS badges) meet your security requirements? If not, would background check costs be passed to the subcontractors?	This project will not accept any workers listed in the State Sex Offender and Public Protection Registration Program. For more information please see section D (Standard scope inclusions), item 18 of the scopes of work. Any expense should be included in your bid number, if any.	Metcon	6/27/2024		Pre-Bid
23	6/27/2024	BIM	Do the submittal drawings have to be in BIM?	Submittal drawings can be in 2D.	Metcon	6/27/2024		Pre-Bid
24	6/27/2024	Scope	Will there be an audio-visual package for this project?	No, there will not be an audio-visual package for this project.	Metcon	6/27/2024	BP1152	Pre-Bid
25	6/27/2024	Bid Manual	When will we receive bid documents?	Bid documents have been released to all certified, pre-qualified subcontractors thus far. If you have not received the documents please contact Andrea Avery.	Metcon	6/27/2024		Pre-Bid
26	6/27/2024	Bid Manual	Do the minority business listed in Affidavit A have to be HUB certified?	Yes, they must be pre-certified.	Metcon	6/27/2024		Pre-Bid
27	6/27/2024		The bid bond on the bid manual shows 10%. Can you confirm that this is correct and it's not 5%?	The bid bond for this project is 10%.	Metcon	6/27/2024		Pre-Bid
28	6/27/2024	Logistics	Crane access, will there be only one side access? Looking at the layout, crane access will be tight, and a bigger crane will be needed due to the reach.	There will be multiple access points for cranes to come in, please see the logistics plan and plan accordingly.	Metcon	6/27/2024		Pre-Bid
29	6/27/2024	Scope	Can you state the requirement for ground improvement regarding fire suppression tank?	In preparation for the installation of the fire suppression Tank, deep stone column foundations will need to be installed before concrete foundations can be poured.	Metcon	6/27/2024	BP3161/0780	

RFI LOG METCON Page: 2 of 4

Pamlico County School 6-12 REQUEST REQUEST LOCATION **ANSWER QUESTION RESPONDER** TRADE/SCOPE **REQUEST BY RESPONSE** DATE Plans/Spec/Bid DATE ITEM# General Note Should Read: "Chemistry 1710, Prep 1708B, Prep General Note #2 on the Enlarged Plans and Elevations pages A-408 through A-413 states that only rooms "Chemistry 1718. 2232B, and MS Science 2230" receive wood lab casework. Wood Prep 1708B, Prep 2230B, and MS Science 2230" receive wood lab casework, however the elevations are showing wood lab casework is indicated correctly on elevations. There is an error on casework in additional rooms not called out on this list. Also, room #1718 is actually shown as a Biology Lab and not 6/28/2024 Plans sheet A-413. The sheet is referencing incorrect room numbers in SFL+a 7/2/2024 BP1230 NYCOM 30 Chemistry. There are also multiple other Lab rooms that receive lab equipment (drying racks, safety stations, goggle the view titles. (MS Science 2225 to be MS Science 2230: PREP cabinets, etc.) that aren't on this list of rooms that receive lab casework. Can you please clarify which rooms are to receive 2225B to be PRE 2232B) There are only 2 classrooms and 2 prep wood lab casework? rooms with wood lab casework and phenolic counter tops. BP1020 Specialties mentions Bike Racks and Fire Extinguisher cabinets but does not include those specifications. Are For Fire Extinguisher cabinets specifications please look at Spec Section 6/28/2024 Scope SFL+a 7/2/2024 BP1230 NYCOM 10-44-00. Bike racks are not included in this project. these included in this bid package? Finish Plan A711A doesn't note shades at 1111 (ext. window) nor at 1102 (ext. /int windows). Do these areas receive Plans 32 6/28/2024 Provide Window shade in at Ext. Window 1111 only. SFL+a 7/2/2024 BP1220 CWT shades? Please confirm. 33 6/28/2024 SFL+a 7/2/2024 CWT Plans Finish Plan A715E is noting WT1 shades at doors @ rooms 1502, 1504, 1506. Are shades required at doors? No, they are not. BP1220 No, Bid Bonds are only required for packages \$100,000.00 or grater. Bid 6/28/2024 34 Bid Manual Do all bid packages require bid bond? Metcon BP1220 CWT manula has been updated. Specifications give an allowance for brick, but the elevations call out a basis-of-design manufacturer and color. Should we Use allowance to provide brick that matches the basis of design. 7/1/2024 35 Plans SFI +a 7/2/2024 BP0400 Southeastern Contracting Subsitute requests will be reviewed to match Basis of Design. iust use the allowances as stated? 7/1/2024 Plans A010 wall type 6B1S is hatched like CMU but this is definitely metal stud, correct? Yes! That is a graphic error. This will be corrected in an addendum SFL+a 7/2/2024 BP0400 Southeastern Contracting 37 7/1/2024 Plans Will the brick allowance cover the special shapes such as shown in 9/A511? No. Bid as drawn. SFL+a 7/2/2024 BP0400 Southeastern Contracting Masonry scope item 41d refers to surface mounted expansion joint covers, but this is also scoped in BP0710 item 11d. Surface mounted expansion joint covers and gasket will be removed 38 7/1/2024 Scope Metcon BP0400 Southeastern Contracting Please confirm that this work will be provided by BP0710. form BP0710 (item 11d) Detail 2/A503 shows foam insulation below finished floor. If we can install an equivalent thickness of rigid foam board at this 7/2/2024 39 7/1/2024 Plans No. Bid as drawn. SFL+a BP0400 location, we can install the outer and inner masonry wythes at the same time, thus eliminating any chance of debris or mud Southeastern Contracting getting on the foundation. Please advise if this is acceptable. 7/1/2024 Scope Yes. SFL+a 7/2/2024 BP0400 Southeastern Contracting Will a mockup be required on this project? If so, can we get details? 41 7/1/2024 Specifications Lockers MFG substitution request. Not Complete - Provide Request per Specs. SFL+a 7/1/2024 BP1050 Elite Storage Products Flexco will not be the BOD for the Vented Wall Base. Johnsonite The Div. 9 Specifications call out "Pre-molded" outside rubber corner bases. Basis of design is Flexco and they do not make a will be the BOD for the Vented Wall Base. Flexco will remain the 42 7/2/2024 Specifications pre-molded corner base. There is nothing in the scopes stating that the pre-molded is required. Can you please confirm if pre-SFL+a BP0960 Bonitz BOD for Non Vented Wall Base. - Specs and Drawings will be molded can be excluded (otherwise, Flexco cannot be the basis of Design)? updated. Please clarify line item from tile scope of work: 38. The subcontractor is required to utilize a robotic total station Item 38 on the Tile Scope of Work refers to the use of a robotic 7/8/2024 43 Scope (similar to that offered by Hilti, Trimble, or Leica) for layout, backchecking, verification before installation, and total station which measures both, vertical and horizontal angles Metcon BP0930 Concordia and slopes. This will ensure accuracy of the final installed product. documenting as-built conditions. We would like to be approved as an equal for the products in spec I am wanting to know if we can do a switch from Sheet Applied Air Barrier to Fluid Applied Air Barrier for Spec 072700. Looking 7/8/2024 Scope section 09840+C52:J580 Acoustic Room Components for Pamlico SFL+a BP0750 Eskola at using Henry Airbloc 17MR. I can submit a technical data sheet if needed County School Note on G-002 Building Code Summary in the Fire Protection Architectural details do not show any fireproofing surrounding structural steel framing, however; on G-005, UL Design No.

RFI LOG METCON Page: 3 of 4

D925 shows fireproofing field applied to steel beams. Please clarify on plans, section's and details in the building framing of

The Aluminum Roof Ladders shown on 2/A-445 are not listed in the BP0510 Scope. What package do they belong to? Or, Are

45

46

47

7/8/2024

7/8/2024

7/8/2024

Plans

Plans

Plans

the need for this fireproofing.

they marked incorrectly, and should be prime painted steel ladder?

Please clarify the conflicting Rail Metal Types as shown for Stair #7. Sheet A-443 Details 9 and 2.

Requirements Table states that: ! NOTE: FLOOR ASSEMBLY -

D925 1/G-005 IS FOR RATED ALCOVE LIDS ONLY. This UL

detail is for the solid concrete lid only. No steel structure is rated in

They are in the wrong scope section Metcon to correct.

Revisions will be made. Stair 1, 2, 7 and 8 in mechanical and fire

stiar areas should have painted steel handrails and guardrails.

SFL+a

Metcon

SFL+a

BP0510

BP0510

BP0510

CM Steel

CM Steel

CM Steel

metcon **Pamlico County School 6-12** REQUEST REQUEST LOCATION **ANSWER** QUESTION RESPONSE **RESPONDER** TRADE/SCOPE **REQUEST BY** DATE Plans/Spec/Bid DATE ITEM# I am going through the specs on this project and have found a discrepancy in section 27.00.00. The first sentence in the CAT 6A shall be used as indicated on T-001. The corrected spec Specifications 48 7/9/2024 summary states to use "category 6A" and the rest of the specifications / drawings refer to category 6. What direction would SFL+a BP2600 NC Sound of Goldsboro shall be distributed in the bid addendum. Confirm which are lab fridges (by spec 115300) and which are residential fridges (by spec 113013) as the plans do not 49 7/10/2024 Specifications Lab fridges are located in science prep rooms only. SFL+a BP1230 Nycom distinguish between the two. Along CL- G there are no Curtain Walls on Level 1. All glazing on Ref to 1/A-111F.1. The structural plan 1/S-101F does not match. Structural plan is missing the Curtain Wall Openings L1 on CL-G are SF. Curtain Walls type 7 and 8 are shown on A-CM Steel 50 7/10/2024 Plans SFL+a BP0510 as shown on the Arch. Floor Plan along grid G. 112F.1. They are shown only on Level 2. The only reference to concrete equipment pads that I see is in the Mechanical General Notes on sheet M-001 and it only Yes, coordination with mechanical contractor will be needed for 51 7/10/2024 Plans states the requirement to confirm pad sizes, and locations in relation to floor drains. Typically, the mechanical contractor Metcon BP2300 TA Woods installation of concrete equipment pads. will coordinate pad locations to be installed by the concrete contractor. Is that the direction we are going on this project? Due to the tight 45 day schedule on the demo/abatement can the abatement be completed over holidays and breaks Yes, abatement can be completed over summer breaks and 52 7/10/2024 Schedule Metcon BP0240 DH Griffin during the school year? holidays. Please refer to schedule for more details. We will provide plan views denoting shear wall locations and Will SFLA and the Engineer of Record provide a Structural Shear Wall plan, Elevations, Wall Sections and Details for 53 7/10/2024 Plans corresponding sections/details. Wall elevations will not be CM Steel Bennett & Pless BP0510 this project. provided. This will be incorporated in a future Addendum. 7/10/2024 Specifications Substitution Request for Wall Panels Not Complete - Provide Request per Specs. SFL+a BP0950 Acousti Spec section 098400 2.3 B 7 d 1) states Factory applied paint. Just below it for 2) states Field Applied. Are the 7/10/2024 Specifications Field Painted. Specification will be udpated to reflect. SFL+a BP0950 Acousti Cementitious panels to be factory or field painted? Please advise on missing specification 7/11/2024 Specifications Specification to be provided. SFL+a BP2700 Strategic Connections 2.7 COMMUNICATIONS COPPER HORIZONTAL CABLING Comply with requirements for identification products in Section 271513 "Communications Copper Horizontal Cabling." We would like to be approved as an equal for the products in spec section 098400 Acoustic Room Components for 7/11/2024 Specifications Not Complete - Provide Request per Specs. SFL+a BP0950 AVL Pamlico County School

METCON RFI LOG Page: 4 of 4









Agenda



- **O ABOUT METCON**
- **O PROJECT TEAM**
- KEY DATES
- LINES OF COMMUNICATION
- PROJECT INFORMATION
- MWSBE COMPLIANCE & WORKFORCE DEVELOPMENT
- **O HUB CERTIFICATION**
- **O PREQUALIFICATION**
- **O BID DOCUMENTS**
- **O QUESTIONS / COMMENTS**

About Us Metcon

ABOUT US





Established in 2000



Headquartered in Pembroke, NC



103 Employees



Divisions: Charlotte, Raleigh, Infrastructure



Completed over 800 projects



Focused on K-12 projects



Over 40 Successful CMAR projects in Eastern North Carolina




Strong Subcontractor Relationships



Project Team

Introduction to the Project Team





Dr. Jeremy Johnson - Superintendent

Design Team

Architect



Civil Engineer

Robert M Chiles Engineering

Plumbing/Mechanical/Electrical Engineer/Technology Design

Optima Engineering

Structural Engineer

Bennett & Pless

Acoustical Engineer

Stewart Acoustical Consultants

Food Consultant

Foodesign Associates, Inc.

Roofing Engineer

REI Engineers

Introduction to the Project Team



Brandon Harper Preconstruction Director

bharper@metconus.com

910.521.8013

Tom Key Sr. Preconstruction Manager

tkey@metconus.com

919.901.8581

Andrea Avery Preconstruction Manager

aavery@metconus.com

912.656.1136

Benjamin McKinney Project Engineer

bmckinney@metconus.com

336.613.3507

Tina Harris Prequalification Manager

tharris@metconus.com

910.521.8013

Jason Deans HUB Director

jdeans@metconus.com

980.253.5799

CONSTRUCTION

Thomas Plant Vice-President

tplant@metconus.com

PRECONSTRUCTION

919.322.2220

Michael Konieczka Project Executive

mkonieczka@metconus.com

919.322.2220

Henry Rivera
Project Manager

hrivera@metconus.com

910.322.2220

Jason Jackowitz Safety Director

jjackowitz@metconus.com

704.284.7717

Key Dates

Key Dates – Bid Dates



Pre-Bid	06.27.24
Last Day for RFI	07.12.24
Last Addendum	07.18.24
BID DAY	07.25.24
Rebid (If Needed)	08.01.24
Tentative NTP (Notice to Proceed)	10/2024
Building Completed	05/2026
Occupancy	08/2026







Project Information – Tentative Milestone Dates



Bid Day	August/7/2024		
Re-Bid Day	August/14/2024		
NTP	October/8/2024		
Building Complete	May/6/2024		
Demo & Parking	June/15/2024		
Punch	August/7/2024		
Occupancy	August/19/2024		

Lines of Communication



ALL COMMUNICATION SHALL GO THROUGH METCON-CONSTRUCTION MANAGER

HUB/MWBE PARTICIPATION QUESTIONS: SEND TO

JDEANS@METCONUS.COM OR CALL JASON DEANS (980) 253-5799

PRE-QUALIFICATION QUESTIONS: SEND TO

THARRIS@METCONUS.COM OR CALL TINA HARRIS (910) 521-8013

ALL RFI'S: SEND TO

<u>AAVERY@METCONUS.COM</u> OR CALL ANDREA AVERY (919) 322-2220 OR Send through Building Connected.

Project Information

Key Dates – Bid Dates



Pre-Bid	06.27.24
Last Day for RFI	07.12.24
Last Addendum	07.18.24
BID DAY	07.25.24
Rebid (If Needed)	08.01.24
Tentative NTP (Notice to Proceed)	10/2024







Bid Packages



- GENERAL TRADES
- FINAL CLEANING
- CAST-IN-PLACE CONCRETE
- DEMO & ABATEMENT
- CONCRETE
- HOLLOW CORE PLANKS
- MASONRY
- STRUCTURAL STEEL
- ORNAMENTAL METALS
- DAMPROOFING & WATERPROOFING
- EIFS
- WALL PANELS
- ROOFING
- FIRE & SMOKE PROTECTION
- DOORS, FRAMES, & HARDWARE
- SPECIALTY DOORS
- STOREFRONT
- METAL FRAMING & GYPSUM BOARD
- HARD TILE
- ACOUSTICAL CEILINGS & PANELS
- RESILIENT FLOORING & CARPET
- ATHLETIC FLOORING

- EPOXY FLOORING
- PAINTING & COATINGS
- VISUAL DISPLAY UNITS
- SIGNAGE
- INTERIOR SPECIALTIES
- STORAGE SPECIALTIES
- AWNINGS & CANOPIES
- FOOD SERVICE EQUIPMENT
- ATHLETIC EQUIPMENT
- WINDOW TREATMENTS
- CASEWORK (MANUFACTURED, COUNTERTOPS)
- TELESCOPIC BLEACHERS
- ELEVATORS
- FIRE SUPPRESSION
- PLUMBING
- HVAC
- ELECTRICAL
- COMMUNICATIONS
- TURNKEY SITEWORK
- DEEP FOUNDATIONS/GROUND IMPROVEMENT
- FENCE & GATES
- LANDSCAPING (PLANTING & IRRIGATION) & SITE FURNISHINGS

Project Information




- Approx. 142,000 SF building
- Two-story with a Mechanical Room on Roof.
- Steel Framed structure with Metal Framing, Masonry and Hollow core planks.
- Exterior skins with Masonry, Metal Wall Panels, Curtainwalls, EFIS
- Interior Finishing such as Carpet Tile, Polished Concrete, Epoxy, Tile








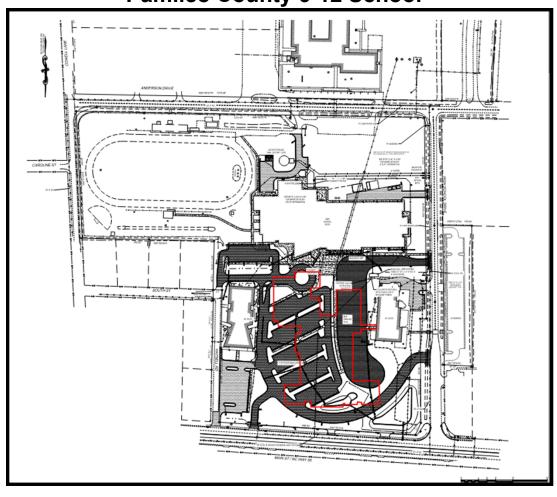


Project Information – Site Logistics Phase 1



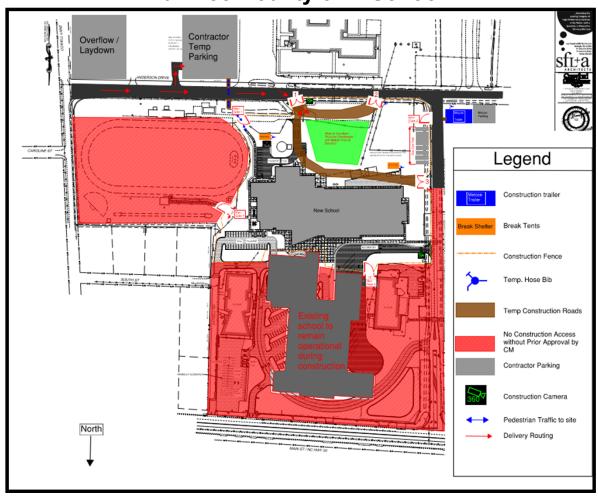


Project Information – Site Logistics Phase 2



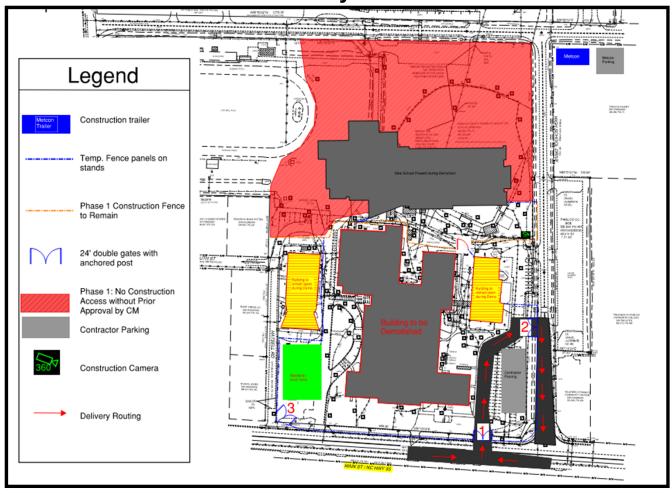

Project Information – Structural Isometric




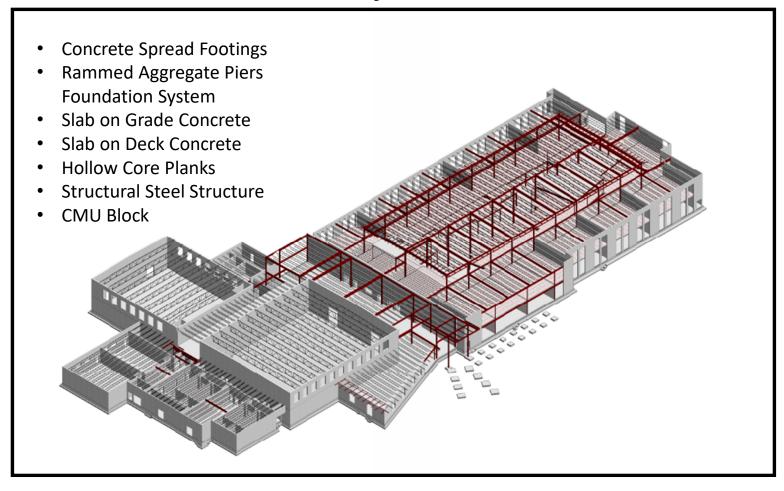

Project Information – Concrete Footings over Rammed Aggregate Piers



- Vibro Pier (VP) system to support the column and wall foundations
- Surcharge the site with structural fill for one month by bringing up the slab to the subgrade elevation

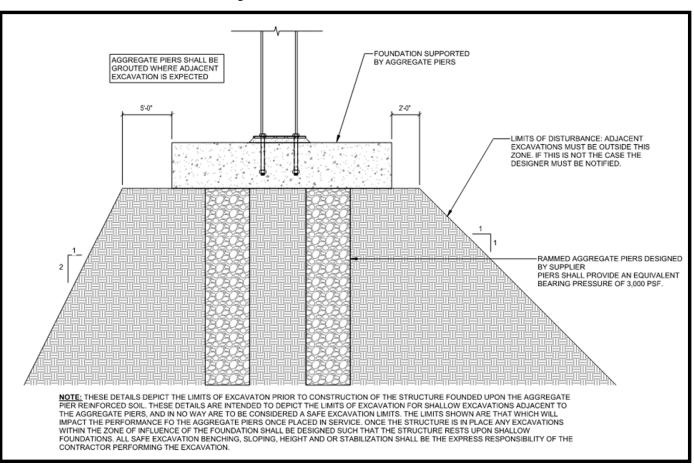

Project Information – First Floor




- Floor & Wall Tile
- Carpet Tiles
- Carpet Sheet
- Luxury Vinyl Tile
- Rubber Athletic Flooring
- Wood Athletic Flooring
- Sealed Concrete
- Resinous Flooring



Project Information – Second Floor



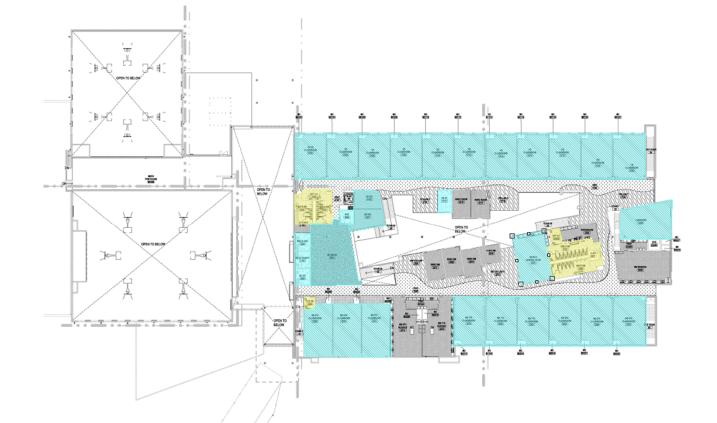


- Floor & Wall Tile
- Carpet Tiles
- Carpet Sheet
- Luxury Vinyl Tile

Project Information – Roof & Canopy



Pamlico County 6-12 School

- Thermoplastic-polyolefin (TPO) membrane. W20yr
- Roof Alternate (9):
 Bituminous membrane
 system, 2 plies of asphalt
 elastomeric membrane with
 polyester and /or fiberglass.
- Alternate (1A):Add walkway canopy.
- Alternate (1B): Add Drop off Canopy

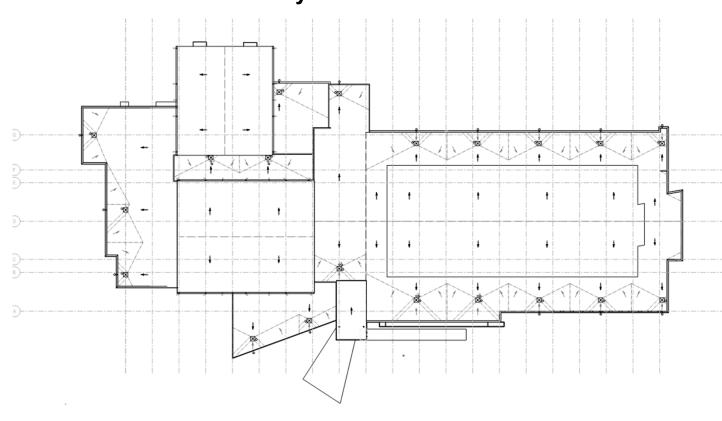




ROOF AREA : 92,397

Project Information – Exterior Elevations (North & South)






- **EIFS**
- Metal Wall panels
- Brick
- Canopies (Alternate) •
- **Spandrel Panels**
- Store Front Glazing Overhead Rolling Doors



Project Information – Exterior Elevations (East & West)



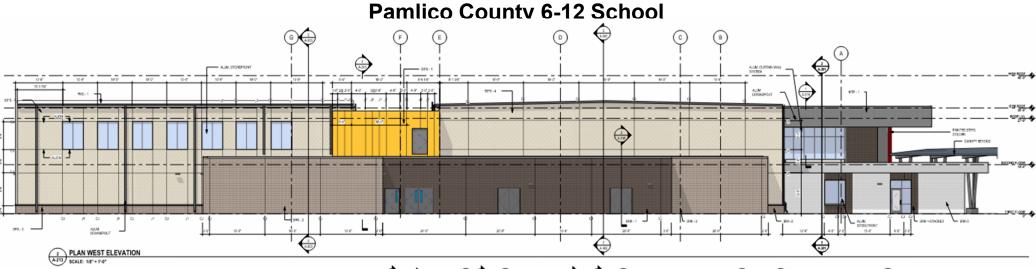

- EIFS
- Metal Wall panels
- Brick
- Canopies (Alternate)
- Store Front Glazing
- Spandrel Panels
- Overhead Rolling Doors



Project Information – Photovoltaic System



Alternate (3): Add Solar PV.


- provide a complete 511kw dc photovoltaic system
- Qcells q.peak duo xl-g10.3/bfg 480w series modules or equal by Trina solar or Sunpower
- Modules shall be mounted on self ballasted rack system with 10 degree tilt.
- Solar edge inverters shall be located in the electrical rooms.

Alternate (4): Add electrical Vehicle Chargers.

- Provide atom power dual port, level 2, 208v, 1-phase electric vehicle charging station, or equal by siemens or Bosch.
- Charger shall be compatible with Atom Power Purple Smart Panel system.

Pamlico County 6-12 School

ALTERNATE NO. 03: PROVIDE A COMPLETE STIKW DC PHOTOVOLTAIC SYSTEM UTILIZING QCELLS Q.PEAK DUO XL.G10.3/BFG 480W SERIES MODULES OR EQUAL BY TRINA SOLAR OR SUNPOWER. MODULES SHALL BE MOUNTED ON SELF BALLASTED RACK SYSTEM WITH 10 DEGREE TILT.SOLAR EDGE INVERTERS SHALL BE LOCATED IN THE ELECTRICAL ROOMS.

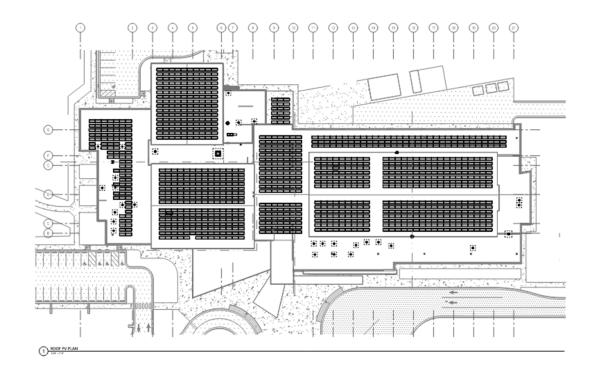


Project Information – Electrical, Communication, Fire & Smoke Protection



Pamlico County 6-12 School

Refer to the following division Specs for this package:

- Division 26 Electrical
- Division 27 Communications: basic telecommunication, cable trays, grounding, identification, com. racks, PA system, Optical Fiber Backbone Cabling, Emergency Responder Radio.
- Division 28 Electronic Safety and Security
- Alternate (7): Refer to Technology
 Drawings. Replace cable trays with J Hook assembly for Technology wiring throughout the building.

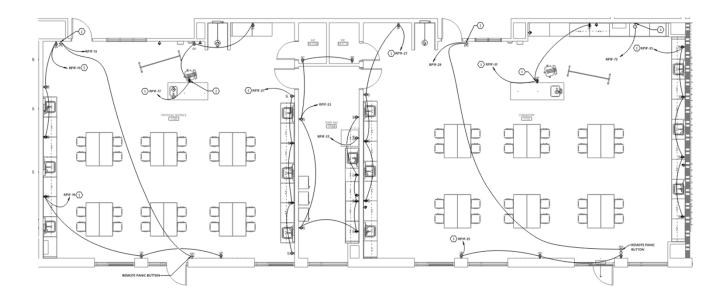

GENERAL NOTE

SEE FLOOR PLANS FOR CIRCUIT DESIGNATIONS
. SEE MANUFACTURER SUBMITTED DRAWINGS FOR EXACT DEVICE


AND CABLING LAYOUTS

1) ENLARGED POWER PLAN - PHYSICAL SCIENCE / CHEMISTRY

Project Information – Plumbing




- Sanitary Below grade (Cast iron hub and s with compression Joints.)
- Sanitary Above grade (Cast iron no HUB)
- Below grade Domestic water (provide typesoft annealed seamless copper tubing)
- Above grade Domestic water (provide typ hard drawn seamless copper tubing and ca copper alloy fittings)
- Turnkey Duplex Lift Station
- Domestic Booster Pump
- Grease Interceptors

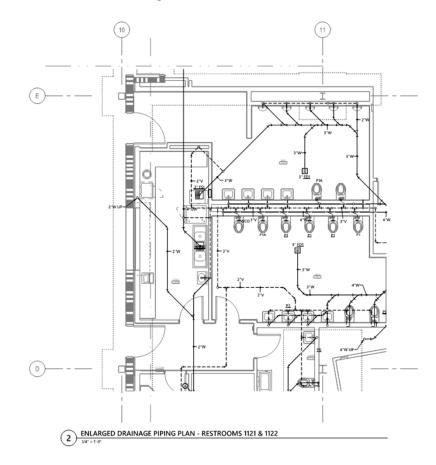

Project Information – Mechanical




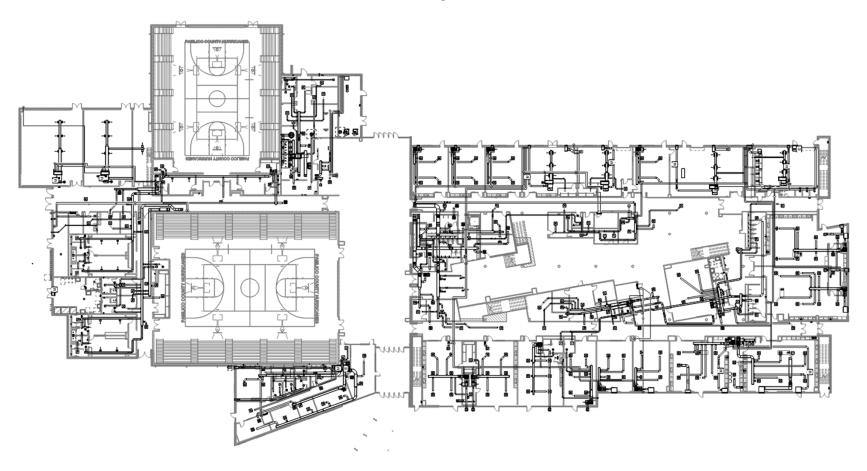


Project Information – Mechanical



Pamlico County 6-12 School

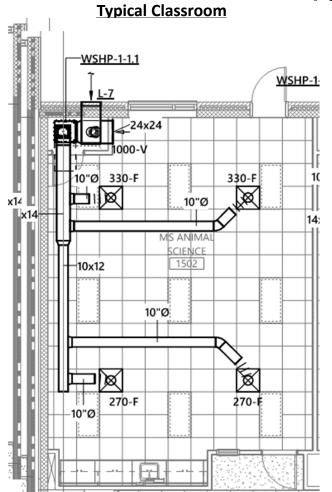


Common Area

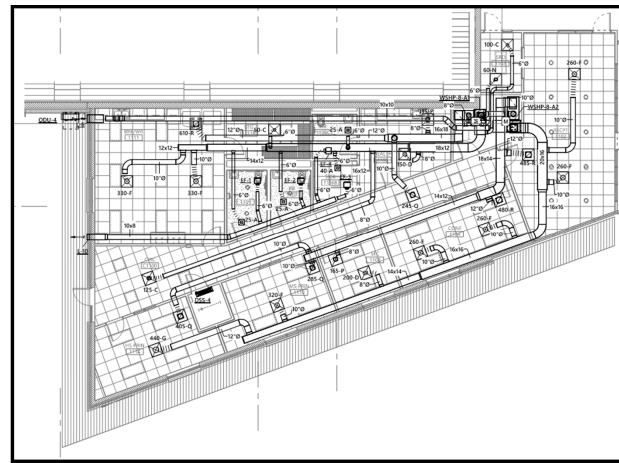

Project Information – Mechanical Geothermal Wellfield



Pamlico County 6-12 School

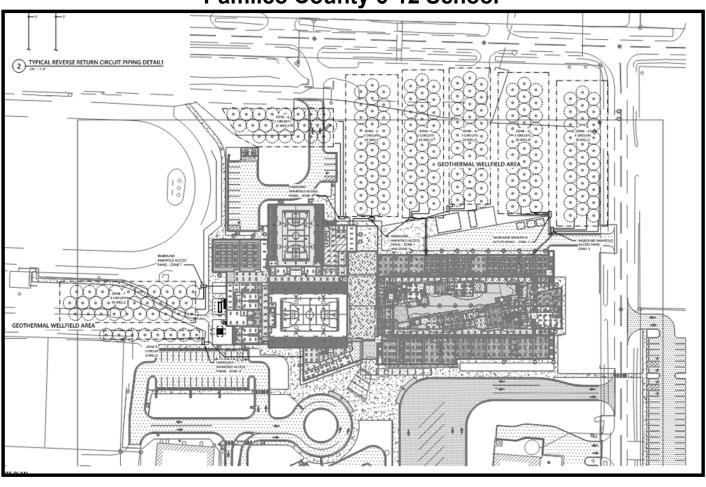

Safety & Health Guidelines



Metcon Robust Safety Program



1 of 26 in NC in OSHA Building Star Program!

- ✓ OSHA Building Star
- ✓ Safety Submittal Review/Approval
- ✓ Trade Partner Kick-off meeting
- ✓ Site Safety Orientation
- ✓ Trade Partners/ Worker Involvement
- ✓ Informal Training
- ✓ Safety Committee
- ✓ Safety Recognition Program
- ✓ Covid-19 Guidelines





Safety Submittals Review/Approval

TASK	POTENTIAL HAZARDS	CONTROLS/PPE
istallation of HVAC equipment uctwork, grilles, legisters.	Cuts, scrapes, lacerations, pirch points, dust in eyes	wear appropriate PPE at all time including had hat, safety west, sefety glasses, safety shoes, long
USULATING DUCT WORK,)	sleeves and pants, and wear appropriate gloves for the took.
	Noise from other trades	Use hearing protection
	DRILLING INTO CONCERTE SUS.	VERIFY BENEATH COMCRETE PLICATO DE
	Slips, trips, falls	Practice good house keeping - keep walking isks clear.
	lifting haronds - hurt back	Use proper lifting technique Use legs, not back. Get kelp.
	Fall Hazards	Use ladders where possible. Utilize half protection if over 6' high. Fill out required
		fall protection plan documentate Inspect scissor lifts daily if used on site.



Safety Training Certification

DUKE ENERGY.	ntractor Chemical Control Form	
Contractor/Vendor Name:		ROUTE: Initia
		Contractor
Contractor/Vendor Contact:	Duke Contact:	Duke PM/FM
		EHS
Project:		Facility Contact
Project management requires the use of safe and enviror brought onto the project site. Unused chemicals will be re	moved by the responsible contractor when the job is	
ITEM 1	ITEM 4	
Chemical Name: Manufacture		Manufacturer:
Amount brought on site (lbs.): Removed from SDS attached – SDS name:		s.): Removed from site:/_
To be used for:		8:
Storage Location: Waste Gen (*	YAN Storage Location:	Waste Gen (Y/N)
ITEM 2	ITEM 5	71000 Oell (174)
Chemical Name: Manufacture		
Amount brought on site (lbs.): Removed from		Manufacturer:
		Manufacturer:
	n site:/ Amount brought on site (Ib	s.): Removed from site:/_
SDS attached – SDS name: To be used for:	n site:/ Amount brought on site (lb SDS attached – SDS name	

Chemical Control Form



Sub Pre-con Kick-off Meeting

ate/Time 4/17/16 b/Task HVAC Installation	Job Hazard Analysis (JHA) Prepared By (Supervision) Matt Tempt	le/Randy Measalt
TASK	POTENTIAL HAZARDS	CONTROLS/PPE
Installation of HVAC equipment, ductwork, grilles ! legisters.	Cuts, scrapes, lacerations, pirch points, dust in eyes	wear appropriate PPE at all time including hard hat, safety vest, safety glasses, safety shoes, low
INSULATING THAT WORK .)	sleeves and pants, and wear appropriate gloves for the took
	Noise from other trades	Use hearing protection
	DRILLING INTO CONCRETE SUB.	VERIER BENEATH CONCRETE PRIDATE D
	Slips, trips, falls	Practice good house keeping Keep walking isks clear.
	lifting hazords - hunt back	Use proper lifting technique Use legs, not back. Get help
	Fall Hazards	Utilize fall protection if over high. Fill out required
	V	fall protection plan documents Inspect scissor lifts daily i






^{*}Attended by Subcontractor Project Manager & Superintendent /Metcon's Project Team and EHS



Safety Monitoring Awareness

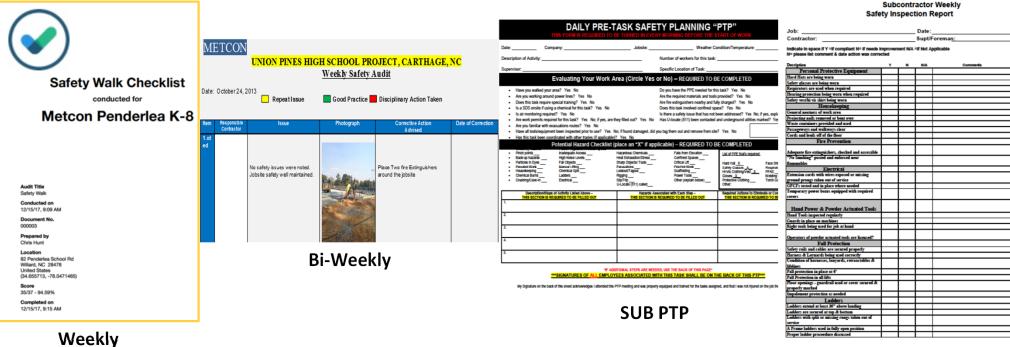

SUB weekly safety audit

MWSBE Compliance and Workforce Development



Project Goals



Help us EXCEED our goal!

20% MWSBE

- ✓ Assist with prequalification
- ✓ Identify subcontracting opportunities
- ✓ Information sharing
- ✓ Virtual Compliance workshop
- ✓ Matchmaking
- ✓ Certification Assistance

MWSBE Compliance and Workforce Development





- Prequalification Assistance How-To's
- Scope Review/Take Offs Pre & Post Bid Help
- Tailor Scopes/Bid Packages
 Smaller Packages
- Teaming Agreements 1st & 2nd Tiers
- Reduced Bond Amounts
- Post –Bid Instruction
 Submittals, Pay Apps, RFI's
- Training Safety & Various Workshops

MWSBE Compliance and Workforce Development





Contractor's College

Understanding HUB Certification

- Ensures all Local/MWBE Get NC HUB Certified
- Understanding "How to Get Prequalified"
- The Process/forms for NC CMAR

Bid Packages and Scopes of Work Workshop

- Estimating & Bid Procedures for NC CMAR
- Understanding Your Scope of Work:
- What all is included in your price?
- Making sure you understand the scope things to watch out for
- Breaking down the specifications, scope of work to prepare a proper bid

Matching 2nd and 3rd Tier Firms with Prime Contractors Event /Bonding Agents

- Strategies for Building Relationships and Bonding Capacity
- Strategies to maximize HUB/MWBE Participation for Each Bid Package





TOOLS FOR SUCCESS

Minority Trade Associations

United Minority Contractors of NC

Contact: Brenda Pollard Phone: 919-817-8626

Address: 5 W Hargett Street, Ste 311, Raleigh, NC 27601

Website: https://umcnc.org

Office for Historically Underutilized Businesses 1336 Mail Service Center Raleigh, North Carolina 27699-1336

Call 984-236-0130

Email: huboffice.doa@doa.nc.gov





MWSBE Compliance and Workforce Development

Involving the **Community** in a Meaningful Way

- Strengthen the workforce pipeline on all fronts
- Align Trade Partners and Community Partners
- Develop a Centralized Outreach/Recruit Forum
- Pre-apprentice Participants
- Major Primes to present list of job openings [full, part-time, temporary] Upon Award
- Participate in Career Fair/Training Events
- Increase Construction Labor Force in NC

Involving the community in meaningful ways



Awareness | Opportunity | Putting People to Work

- Metcon's Community and Education Foundation
- Connect Youth to Jobs & Training in Construction Career Fairs, Apprenticeships
- Make Career Connections on Your Project
- Work Force Development
- Establish Partnerships in the Community
- Re-entry Work Program







HUB Certification



Certification on the HUB Office Website

HUB Office website:

https://ncadmin.nc.gov/businesses/hub

Announcements



Save the Date!

2023 NC Statewide MED Week Celebration - October 31, 2023

Certifications have moved online!

Start the certification process at https://evp.nc.gov/

Ready to learn?

The HUB Office offers a number of training resources, including a library of webinars. Check them out!

Register for outreach and training events.



Interested in becoming certified through the HUB Office?

The NC HUB Office offers a Statewide Uniform Certification (SWUC; aka HUB certification) and an NC Small Business Enterprise (NCSBE) certification.

Quick Links

State of NC Disparity Study

Submit Solicitation Opportunities

Request HUB outreach/training

About HUB/HUB Legislation

Governor's Advisory Council on HUB

Contact Us

Prequalification

Project Prequalification Submittal (Part A)



	Part A: Master Prequalification Form (Annual Submittal) must be provided
	rill expire on June 30 th of each year and requires an update after July 1 th . If the rejected. A separate Part B: Project Specific Supplement is required for
each specific project. Part A and Part B will be evaluated	ted together for the specific project.
Part A: Master Prequalification (Annua	l Submittal)
Submittal Date:	
Expiration Date:	
Submitted to:	(Name of CM at Risk firm)
1. Main Office Location & Company Co	ontacts
Company Name	
Company Hame	
Physical Address	
Mailing Address	
City/State Zip Code + 4	
() Phone number	[ax number
Phone number	Pax number
President/CEO	CFO
Primary Prequalification Contact Name	Primary Prequalification Contact Phone Number
Primary Prequalification Contact Email Address	Company Website
Secondary Prequalification Contact Name	Secondary Prequalification Contact Phone Number
Secondary Prequalification Contact Email Address	
2. Business Type	
(check box) Corporation Partnership Limite	ed Liability Company Sole Proprietor
Indicate your NC Statewide Uniform Certification:	(check box):
MBE 🛮 HBE 🗈 AABE 🖺 AIBE 🗓 WBE 🗀 SDB 🗆 DBE	
See website link for more information: http://www	v.doa.nc.gov/hub/swuc.htm
	Secretary of State to conduct business in the State of North Carolina?
Is your firm registered with the Department of the	
Is your firm registered with the Department of the ☐ Yes ☐No	
	other organization? Tyes II No

Part A: CM at Risk 1st Tier Sub Master Prequalification Form (Annual Submittal)

- 1. Main Office Location & Company Contacts
- 2. Business Type
- 3. Licensing Information
- 4. Type of Scope of Performed
 - Completed Projects
- 5. Size of Company (Past 5 years)
- 6. Current Workload
- 7. Safety
 - EMR Ratings Experience Modification Ratings
 - RIR Ratings Recordable Incident Rate
 - DART Days Away Restricted or Transferred
 - OSHA 300 Reports
- 8. Litigation, Claims, Criminal Convictions
- 9. HUB HUB Plan
- 10. Signature

Required Supplemental Information Needed for Part A

- Recent Audited or Reviewed Financial Statements
- Bonding Letter
- COI
- EMR from Insurance Company
- OSHA 300 Reports
- Copy of HUB Certification
- Copy of Professional Licenses (If Applicable)

Project Prequalification Submittal (Part A) – TRADE TAPP





PUBLIC LINK TO QUALIFY

The public link to qualify can be added to your company's website for subcontractors to self-invite and complete your questionnaire. As a helpful reminder, each invite utilizes qualification point(s). Questions?

Reach out to support

http://app.buildingconnected.com/_/risk/public-invite/5913920ece945d0a00d28670

Project Prequalification Submittal (Part B)



Part B: CM at Risk 1st Tier Subcontractor Prequalification (Project Specific Supplement)

	s Part B may be used as a project specific "short form" supplement to the prequalification is submitted to the CMAR a "Complete" Master Prequalification Package Part A during the						
	s submitted to the CMAR a Complete Master Predualification Package Part A during the project specific pregual advertisement						
	complete" Master prequal Part A submitted to the CMAR dated//20remains in						
good standing for the overall accuracy of the subcontractor for the fiscal period. Yes No If no, explain the material changes							
	ny size, licenses, type of work performed, financials, bonding, insurances, litigation, etc.:						
	requal, the CMAR may require Subcontractor to submit an updated Master Prequal and reject this supplement)						
1. Information							
	me:						
1.b.1 Primary Contact Full Na	ame:						
1.b.3 Primary Contact email							
	d Exhibit 1 (Listing of Bid Packages) to indicate which Bid Packages this lalify for on this Project and return with Prequalification Part B.						
	artner or Joint Venture with another Subcontractor for this Project: VES No						
	their applicable participating percentage:						
yes, list the Companies involved and	their applicable participating percentage:						
2. Updated Company Inform	nation (from Part A; Master Prequalification Form)						
2. a. Update your Current Backlog \$	(unearned revenue as of date of this supplement)						
2. b. Attach updated Bonding letter	from your Surety if anticipated Bid Package will exceed \$300,000. Letter shall be						
dated within the last 30 days. Have y	rou attached a surety letter? ☐ Yes ☐ No						
2.c. Attach a list to Part B of all the P	rojects working with the CM at Risk of the Project in the last 5 years						
3. Project Specifics							
3.a. The assigned project superinten	dent for this projectshall be:						
Include a resume. Have you included	l a resume? 🛮 Yes 🗈 No						
3.b. Experience of the superintender	nt on this specific type of project is: 0-2 3-4 5-10 >10 years.						
3.c. The assigned project manager for	or this project shall be						
Include a resume. Have you included	l a resume? Yes No						
3.d. Experience of the project manag	ger on this specific type of project is:0-23-45-10>10 years.						
	ted projects of similar type which most closely reflects the size and complexity of						
	r the currently proposed project within the last 5 years.						
#1 –Similar Project Name (Size /							
Scope / over 50% Competed)							
Description of Work Performed							
Completion Date (or expected)							
Owner Name/ Representative							
Owner Address/Phone #/Email							
Architect Name/Representative							
Architect Address/Phone #/Email							
GC or CM Name/Representative							
GC or CM Address/Phone #/Email							
Contract Dollar Value							
Percentage Complete							
HUB Percentage Achieved							
1100 i ci celitage Acilieved							

Part B: CM at Risk 1st Tier Subcontractor Prequalification (Project Specific Supplement)

Description of Work Performed	
Completion Date (or expected)	
Owner Name/ Representative	
Owner Address/Phone #/Email	
Architect Name/Representative	
Architect Address/Phone #/Email	
GC or CM Name/Representative	
GC or CM Address/Phone #/Email	
Contract Dollar Value	
Percentage Complete	
HUB Percentage Achieved	
#3 –Similar Project Name (Size / Scope / over 50% Competed)	
Description of Work Performed	
Completion Date (or expected)	
Owner Name/ Representative	
Owner Address/Phone #/Email	
Architect Name/Representative	
Architect Address/Phone #/Email	
GC or CM Name/Representative	
GC or CM Address/Phone #/Email	
Contract Dollar Value	
Percentage Complete	
HUB Percentage Achieved	
3.f.1.a = supervisors 3.f.1.b = skilled trade 3.f.1.3 = unskilled tra 3.f.2 What is percentage of a	f craft employees does Subcontractor employee for Bid Packages requesting: and foreman =each sersman =each adesman =each multipated self perform work with own forces vs. subcontracting to lower tiers: ouse labor% to outsource ready labor:% lower tier subcontract;
	knowledging that all answers are true to the best of your knowledge. <u>Any answer</u> Im being prequalified on this proiest.
Dated this day of:	


Page 2 of 3

Part B: CM at Risk 1st Tier Subcontractor Prequalification (Project Specific Supplement)

Check	Preliminary	Como of Words	D/ 4
BP	Package	Scope of Work	Bid
	BP017000	FINAL CLEANING	\$ 114,674.00
	BP017100	GENERAL TRADES	\$ 413,996.00
	BP024000	DEMO	\$ 720,000.00
	BP033000	CAST-IN-PLACE CONCRETE	\$ 2,324,972.00
	BP340000	PRE-CAST CONCRETE	\$ 1,434,391.00
	BP042000	MASONRY	\$ 3,459,150.00
	BP051000	STRUCTURAL STEEL	\$ 3,591,000.00
	BP052000	MISCELLANEOUS METALS	\$ 363,150.00
	BP0618000	GLU-LAM	\$ 909,900.00
	BP071000	WATERPROOFING, JOINT EXPANSION & EXPANSION JOINTS	\$ 171,810.00
	BP0724000	EFIS	\$ 506,250.00
	BP074000	WALL PANELS	\$ 553,095.00
	BP075000	TURNKEY ROOFING	\$ 2,150,586.00
	BP081000	DOORS, FRAMES, & HARDWARE	\$ 548,280.00
	BP083000	SPECIALTY DOORS	\$ 67,500.00
	BP084000	STOREFRONT	\$ 3,271,612.00
	BP092000	METAL FRAMING & GYPSUM BOARD	\$ 1,526,874.00
	BP093000	HARD TILE	\$ 36,610.00
	BP095000	ACOUSTICAL CEILINGS	\$ 535,343.00
	BP095100	ACOUSTICAL WALL PANELS	\$ 155,029.00
	BP096000	RESILIENT FLOORING & RESILIENT ATHLETIC FLOORING	\$ 757,170.00
	BP0964000	ATHLETIC FLOORING - WOOD FLOORING	\$ 230,076.00
	BP096700	EPOXY FLOORING	\$ 197,416.00
	BP099000	PAINTING & COATINGS	\$ 395,814.00
	BP101000	SIGNAGE	\$ 89,099.00
	BP101100	VISUAL DISPLAYS	\$ 103,499.00
	BP102000	INTERIOR SPECIALTIES & PARTITIONS	\$ 179,195.00
	BP102200	OPERABLE PARTITIONS	\$ 58,500.00
	BP105000	STORAGE SPECIALTIES	\$ 176,400.00
	BP107300	AWNINGS & CANOPIES	\$ 511,200.00
	BP11400	FOOD SERVICE EQUIPMENT	\$ 696,433.00
	BP116100	STAGE EQUIPMENT	\$ 180,000.00
	BP116600	ATHLETIC EQUIPMENT	\$ 144,166.00
	BP122000	WINDOW TREATMENTS	\$ 108,000.00
	BP123000	CASEWORK	
	BP126100	FIXED AUDIENCE SEATING	\$ 270,000.00
	BP126600	TELESCOPIC BLEACHERS	\$ 304,258.00
	BP142000	ELEVATORS	\$ 139,500.00
	BP210000	FIRE SUPPRESSION	\$ 752,551.00
	BP220000	PLUMBING	\$ 2,114,310.00
	BP230000	HVAC	\$ 6,163,749.00
	BP260000	ELECTRICAL	\$ 5,692,500.00
	BP310000	TURNKEY SITEWORK	\$ 4,426,444.00
	BP329000	LANDSCAPING	\$ 270,000.00
	BP330000	SITE UTILITIES	\$ 450,000.00
	BP323000	FENCE & GATES	\$ 90,000.00


Project Prequalification Submittal (Part B) – Building Connected



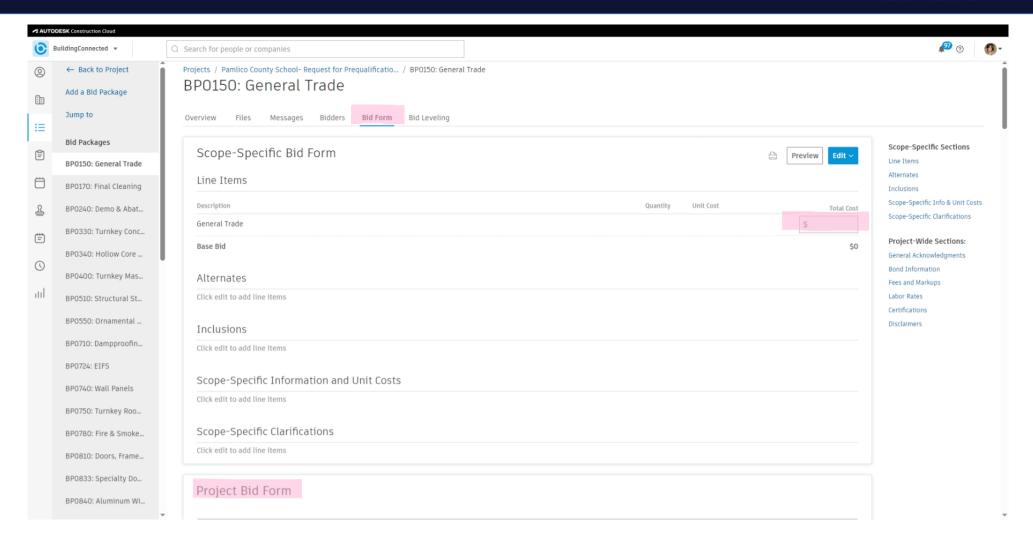

Project Prequalification Submittal (Part B) – Building Connected



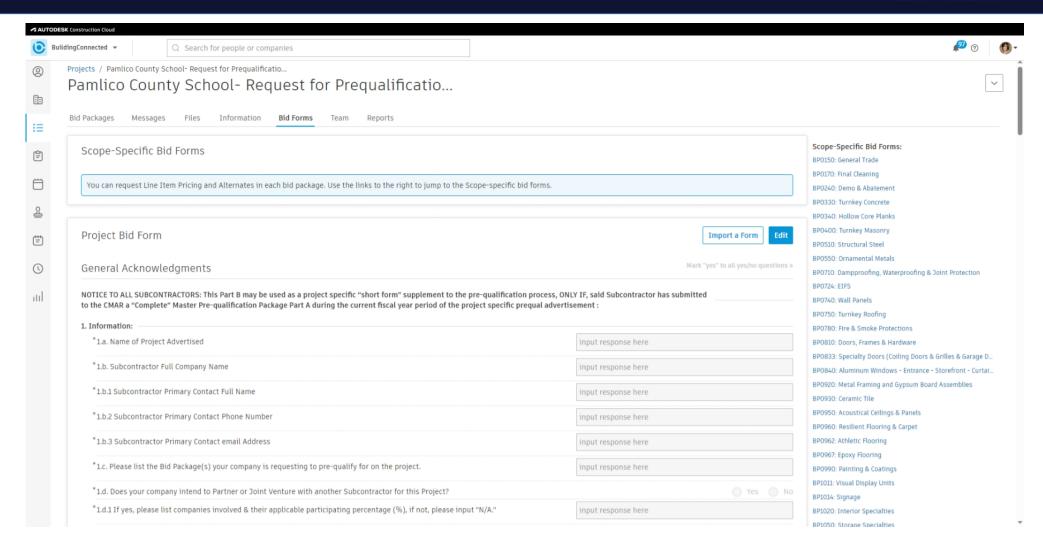

Project Prequalification Submittal



Company Information

- Business Type
- Licensing
- Scope of Work
- Past/Present Project
- Litigations
- Financial
- Bonding
- Insurance/EMR


GRADING MATRIX

TA Section #			t B - Exhibit 2			- d C	NAAD				
Package No. & Description:		Prequalification Ratings Matrix	for First-Tier Sub	contra	ctors u	nder C	WAK				
Package No. & Description:	me of Subcontractor :										
Package No. & Description:	niect Name:										
TA Section #	•										
Visit of No. Pls P	d Package No. & Description:										
NA SECURENT WORKLOAD AL SUPPLEMENTAL INFORMATION AL SUPPLEMENTAL WORKLOAD AL SUPPLEMENTAL INFORMATION AL SUPPLEMENTAL INFORMATIO				1	2	3	4	5	6	7	8
AND STATE OF SCHOPPON TO PORT AT A SUPPRIMENTAL INFORMATION AND A SUPPRIMENTAL INFORMATION A				to to	tor.	tor	tor	tor	tor a	to a	to t
ANT A SECURITY OF NO. 1 1				and trac	a ta	trac	a ta	a frac	a trac	a trac	a rac
Pet Pts Pts Pts Pts Pts Pts Pts Pts Pts Pt				Cont	S S	Cont	S S	Cont	L S	Cont	l in it
THE A-1. DICTIONATION WE OF NO. I THE A-2. BUSINESS TYPE VES OF NO. I THE A-3. DICTIONATION WE A-3. DICTIONATION WE A-3. DICTIONATION WE A-4. TYPE OF SCOPE OF WORK / AVERAGES SIZE / LARGEST PROJECT VES OF NO. I THE A-5. DICTIONATION WE A-6. CURRENT WORKLOAD WE A-6. CURRENT WORKLOAD VES OF NO. I THE A-5. DICTIONATION AVERAGES SIZE / LARGEST PROJECT VES OF NO. I THE A-6. CURRENT WORKLOAD VES OF NO. I THE A-6. CURRENT WORKLOAD VES OF NO. I THE A-6. CURRENT WORKLOAD VES OF NO. I THE A-7. CURRENT WORKLOAD VES OF NO. I THE A-7. CURRENT WORKLOAD VES OF NO. I THE A-6. CURRENT WORKLOAD VES OF NO. I THE A-7. CURRENT WORKLOAD VES OF NO. I THE A-6. CURRENT WORKLOAD V	art A Section #	Description	Yes or No								
AT A - LUCRISHON INFORMATION WE STOR TO COMPANY WE STOR TO COMPA					7.03		7.03	7.0	7.03	- 10	
HE A - 1. DECINING INFORMATION WHA A - 4. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT WHA A - 5. TYPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT SIZE / AVERAGE SIZE / LARGEST PROJECT SIZE / LARGE	A A A DIVINITY TYPE		Was as No								
art A - 1. TIPE OF SCOPE OF WORK / AVERAGE SIZE / LARGEST PROJECT PER A - 5. SIZE OF COMPANY WHA - 6. CURRENT WORKLOAD WHA - 7. CURRENT WORKLOAD WE A - 7. CURRENT WORKLOAD WE A - 7. CURRENT WORKLOAD WE A - 8. LITEGATIONS AND CLAIMS WE A - 8. LITEGATIONS AND CLAIMS WE A - 8. LITEGATIONS AND CLAIMS WE A - 9. RUB OR DIVERSITY PLAN WE OF No. 1 South A - 9. RUB OR DIVERSITY PLAN WE OF No. 1 South A - 9. RUB OR DIVERSITY PLAN WE OF No. 1 South A - 9. RUB OR DIVERSITY PLAN WE OF No. 1 South A - 9. RUB OR DIVERSITY PLAN WE OF No. 1 South A - 9. RUB OR DIVERSITY PLAN WE OF No. 1 South A - 9. RUB OR DIVERSITY PLAN WE OF No. 1 South A - 9. RUB OR DIVERSITY PLAN WE OF No. 1 Current Insurance Certificate meeting OC 15 Article 34 VE OF No. 1 Current Insurance Certificate meeting OC 15 Article 34 VE OF No. 1 Current Insurance Certificate meeting OC 15 Article 34 VE OF No. 1 Copy of International Company Letter Copy of International Company Letter Copy of International Company Letter Copy of International Copy of Internati	PER A - 2. BUSINESS TYPE		Yes or No	1							
art A - 5. SIZE OF COMPANY art A - 6. CURRENT WORKLOAD ves or No ves or No	art A - 3. LICENSING INFORMATION		Yes or No	1							
Author Francis Some South Sout	art A - 4. TYPE OF SCOPE OF WORK / AVE	RAGE SIZE / LARGEST PROJECT	Yes or No	1							
Author Francis Some South Sout											
art A - 7. CURRENT WORKLOAD Ves or No. 1 Audited financials Order of Indian Section 2 Current Insurance Certificate meeting OC-15 Article 34 Use or No. 1 Copy of Hub Certification, if claimed in Section 2 Copy of Libernies for Specific work, if required in Section 3 Part A Acceptance = Subtotal 15 out of 15 points art 8 - 2. UPDATED COMPANY INFORMATION 2a (Current Backlog and Bonding Capacity Available 2 2b List of Projects working with CMAR in last 5 years 9 2c List of Projects working with CMAR in last 5 years 9 3b Released Project Manager resume and experience 4 3c Released Project Supplementary Frequentlying for 7 3c Related Project Supplement of Trade Prequalifying for 7 Part A Acceptance = Subtotal 10 rout of 10 points 10 Ves or No. 1 A Section 8 Description Ves or No. 1 Description Ves or No. 1 A Section 8 Description Ves or No. 1 Description			Yes or No	1							
art A - 8. LITIGATIONS AND CLAIMS Ves or No 1 Audited Financials Bonding Company Letter Current Insurance Certificate meeting OC 15 Article 34 Ves or No 1 Copy of Insurance Foreign Company Letter Copy of Licenses for Specific work, if required in Section 2 Copy of Licenses for Specific work, if required in Section 3 Part A Acceptance = Subtotal 15 out of 15 points Test Of No 15 Part A Acceptance = Subtotal 15 out of 15 points Test Of No 15 Part B - 3. PROJECT SPECIFICS Assigned Superintendent resume and experience Yes or No 1 B Releated Project Manager resume and experience Yes or No 1 A Releated Project Manager resume and experience of Signed Superintendent Tesume and experience of Signed Signed Project Manager Tesume and experience of Signed Signed Project Manager Tesume and experience of Signed Signed Project Manager Ves or No 1 A Released Project Experience of Signed Project Manager Ves or No 1 B A Released Project Experience of Signed Project Manager Ves or No 1 B A Released Project Experience of Signed Project Manager V	art A - 6. CURRENT WORKLOAD		Yes or No	1							
art A - 9. NUB OR DIVERSITY PLAN art A - 5. SUPPLEMENTAL INFORMATION Audited financials Bonding Company Letter Current insurance Certificate meeting OC-15 Article 34 Letter from ins	art A - 7. CURRENT WORKLOAD		Yes or No	1							
Audited Financials Bonding Company Letter Ves or No Current Insurance Certificate meeting OC-15 Article 34 Ves or No Letter from insurance Company stating EMR Ves or No Letter from insurance Company stating EMR Ves or No Sista Not Report Copy of Legoust Part A Acceptance = Subtotal 15 out of 15 points Test B Section 8 Part A Acceptance = Subtotal 15 out of 15 points Test B Section 8 Description Ves or No Test B Section 8 Test B Se	art A - 8, LITIGATIONS AND CLAIMS		Yes or No	1							
Audited Financials Bonding Company Letter Bonding Company Letter Current Insurance Certificate meeting OC-15 Article 34 Ves or No Letter from Insurance Company stating EMR Ves or No City A 1 Letter from Insurance Company stating EMR Ves or No Letter from Insurance Company stating EMR Ves or No Letter from Insurance Company stating EMR Ves or No Letter from Insurance Company stating EMR Ves or No Letter from Insurance Company stating EMR Ves or No Letter from Insurance Company stating EMR Ves or No Letter from Insurance Company stating EMR Ves or No Letter from Insurance Company stating EMR Ves or No Letter from Surance Insurance Company Stating EMR Ves or No Letter from Surance Insurance Company Stating Insurance Company I	art A - 9. HUB OR DIVERSITY PLAN		Yes or No	1							
Bonding Company Letter Current Insurance Carlificate meeting OC-15 Article 34 Letter from Insurance Carlificate meeting OC-15 Article 34 Ves or No Letter from Insurance Carlificate meeting OC-15 Article 34 Ves or No Copy of HUB Certification, if claimed in Section 2 Copy of Leenses for Specific work, if required in Section 3 Copy of Leenses for Specific work, if reported in Section 3 Part A Acceptance = Subtotal 15 out of 15 points Test of No Part A Acceptance = Subtotal 15 out of 15 points Test of No Description Yes or No Pts Pts Pts Pts Pts Pts Pts Pt	art A - SUPPLEMENTAL INFORMATION		_								
Current Insurance Certificate meeting OC-15 Article 34 Letter from Insurance Company statile 24 Copy of Pub Certification, if claimed in Section 2 Copy of Licenses for Specific work, if required in Section 3 Part A Acceptance - Substoat 15 out of 15 points art B - 2. UPDATED COMPANY INFONMATION 2a Current Backlog and Bonding Capacity Available 2b Cattach bonding letter from Surety, if over 5300k 2c (List of Projects working with CMAR in last 5 years The Section Backlog and Bonding Capacity Available 2c (List of Projects working with CMAR in last 5 years The Section Backlog and Bonding Capacity Available 2c (List of Projects working with CMAR in last 5 years The Section Backlog and Bonding Capacity Available 2d (List of Projects working with CMAR in last 5 years The Section Backlog and Bonding Capacity Available 2d (List of Projects working with CMAR in last 5 years The Section Backlog and Bonding Capacity Available 2d (List of Projects working with CMAR in last 5 years The Section Backlog Capacity Available 2d (List of Projects working with CMAR in last 5 years The Section Backlog Capacity Available The Section Backlog Capacit				1							
Letter from Insurance Company stating EMR OSHA MOD Reports Copy of HUB Certification, if claimed in Section 2 Copy of HUB Certification, if claimed in Section 2 Yes or No Copy of HUB Certification, if claimed in Section 2 Yes or No Part A Acceptance = Subtotal 15 out of 15 points The section B Description The section B Description B Pts											
OSHA BORROPITS Copy of Licenses for Specific work, if required in Section 2 Copy of Licenses for Specific work, if required in Section 3 Part A Acceptance = Subtotal 15 out of 15 points art 8 - Section 8 Description Yes or No Pts				1							_
Copy of HUB Certification, if claimed in section 2 Copy of HUB Certification, if claimed in section 3 Copy of Useness for Specific work, if required in Section 3 Part A Acceptance = Subtotal 15 out of 15 points Description Yes or No Pts				1							_
Part A Acceptance = Subtotal 15 out of 15 points Description Yes or No Pts				î							
art 8 Section 8 Description Yes or No Pts		Copy of Licenses for Specific work, if required in Section 3	Yes or No	1							
art 8 - 1. INFORMATION art 8 - 2. UPDATED COMPANY INFORMATION 2a Current Backlog and Bonding Capacity Available		Part A Acceptance = Subtotal 15 out of 15 points		15							
art B - 2. UPDATED COMPANY INFORMATION 2a Current Backlog and Bonding Capacity Available 2b Attach bonding letter from Surety, if over 5300k 2c List of Projects working with CMMR in last 5 years art B - 3. PROJECT SPECIFICS 3a Assigned Superintedent resume and experience 4 Yes or No 3b Relevant project experience of assigned Superintedent 4 Yes or No 1		Description	Yes or No	Pts	Pts	Pts	Pts	Pts	Pts	Pts	Pts
2a Current Backlog and Bonding Capacity Available Yes or No 1 2b Attach bonding letter from Surety, if over \$300k Yes or No 1 2c List of Projects working with CMAR in last 5 years Yes or No 1 3b Relevant project experience of assigned Superintendent Yes or No 1 3c Assigned Project Manager resume and experience Yes or No 1 3c Assigned Project Manager resume and experience Yes or No 1 3d Relevant project experience of assigned Superintendent Yes or No 1 3d Relevant project experience of assigned Project Manager Yes or No 1 3e Related Project Experience Yes or No 1 3f. Available Craftsman for Trade Prequalifying for Yes or No 1 3f. Self performance for Trade Prequalifying for Yes or No 1 3f. Self performance for Trade Prequalifying for Yes or No 1 Part B Acceptance = Subtotal 10 out of 10 points 10											
2b											
2c List of Projects working with CMAR in last 5 years Yes or No 1 art B - 3. PROJECT SPECIFICS 3a Assigned Superintendent resume and experience Yes or No 1 3b Relevant project experience of assigned Superintendent Yes or No 1 3c Assigned Project Manager resume and experience Yes or No 1 3d Relevant project experience of assigned Project Manager of Yes or No 1 3e Related Project Experience Of assigned Project Manager Yes or No 1 3e Related Project Experience Yes or No 1 3f.1 Available Craftsman for Trade Prequalifying for Yes or No 1 3f.1 Self performance for Trade Prequalifying for Yes or No 1 Part B Acceptance = Subtotal 10 out of 10 points 10				1							
art B - 3. PROJECT SPECIFICS 3a Assigned Superintendent resume and experience 3b Resievant project experience of assigned Superintendent 3c Assigned Project Manager resume and experience 3d Resievant project experience of assigned Project Manager 4 Yes or No 3 Resievant project experience of assigned Project Manager 4 Yes or No 5 Assigned Project Manager resume and experience 7 Yes or No 8 Assigned Project Manager 9 Yes or No 1	26	Attach bonding letter from Surety, if over \$300k		1							_
3a Assigned Superintendent resume and experience Yes or No 1 3b Relevant project experience of assigned Superintendent Yes or No 1 3c Assigned Project Manager resume and experience Yes or No 1 3d Relevant project experience of assigned Project Manager Yes or No 1 3e Related Project Experience Area of the Superience Yes or No 1 3e Related Project Experience Area of the Superience Area of		List of Projects working with CMAR in last 5 years	res or No	1							
3b Belevant project experience of assigned Superintendent Yes or No 1		Assessed Consolidated and Assessed Assessed	Yes es No								
3c Assigned Project Manager resume and experience Yes or No 1				1						_	
3d Relevant project experience of assigned Project Manager Yes or No 1 3e Related Project Experience Yes or No 1 31.1 Available Craftsman for Trade Prequalifying for Yes or No 1 31.1 Self performance for Trade Prequalifying for Yes or No 1 Part B Acceptance = Subtotal 10 out of 10 points 10 10 Yes or No 1 11 Yes or No 1 12 Yes or No 1 13 Yes or No 1 14 Yes or No 1 15 Yes or No 1 16 Yes or No 1 17 Yes or No 1 18 Yes or No 1 19 Yes or No 1 10 Yes or No 1 10 Yes or No 1 11 Yes or No 1 12 Yes or No 1 13 Yes or No 1 14 Yes or No 1 15 Yes or No 1 16 Yes or No 1 17 Yes or No 1 18 Yes or No 1 19 Yes or No 1 19 Yes or No 1 10 Yes or No 1 10 Yes or No 1 11 Yes or No 1 12 Yes or No 1 13 Yes or No 1 14 Yes or No 1 15 Yes or No 1 16 Yes or No 1 17 Yes or No 1 18 Yes or No 1 19 Yes or No 1 19 Yes or No 1 10 Yes or No 1 10 Yes or No 1 11 Yes or No 1 12 Yes or No 1 13 Yes or No 1 14 Yes or No 1 15 Yes or No 1 16 Yes or No 1 17 Yes or No 1 18				1							
3e Related Project Experience Yes or No 1	36	Relevant project experience of assigned Project Manager		î							
31.1 Available Craftsman for Trade Prequalifying for Yes or No 1	36	Related Project Experience		î							
Part B Acceptance = Subtotal 10 out of 10 points 10	3f.1	Available Craftsman for Trade Prequalifying for	Yes or No	1							
		Self performance for Trade Prequalifying for	Yes or No	1							
		Part B Acceptance = Subtotal 10 out of 10 points		10							
TOTAL POINTS = 25 points out of 25 points		TOTAL POINTS = 25 points out of 25 points		25							

Bid Documents

Bid Documents- Plans, Bid Manual, Specifications



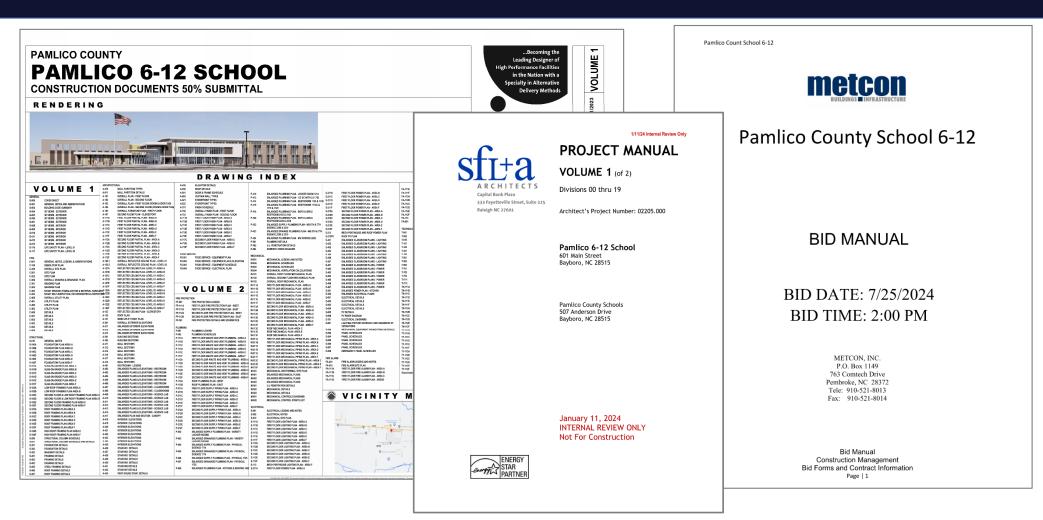

Bid Documents- Plans, Bid Manual, Specifications



Bid Bond Form

metcon CMR 00 43 13 - Bid Bond Form Please use the attached form or AIA-310 with similar listed parties. KNOW ALL MEN BY THESE PRESENTS THAT as principal, and _ as surety, who is duly licensed to act as surety in North Carolina, are held and firmly bound unto the State of North Carolina and , and as obligee, in penal sum of: FIVE, 5% percent of amount of bid or, DOLLARS, lawful money of the United States of America, for the payment of which, well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors and assistances jointly and severally, firmly by these presents. Sealed, signed and dated this _____ day of _ **Bid Checkli** WHEREAS, the said principal is herewith submitting Print Outside Sealed Envelope file this bod bond in lieu of making the cash deposit ☐ Company Name ☐ Project Name ☐ Bid Package Name and Number (i.e., BP08100 I ☐ Bid Enclosed NOW, THEREFORE, THE CONDITION OF THE A principal shall be awarded the contract for which the | cled Envelope | Bid Proposal Form | Bid Bond or Cashier's Check if > than \$300,000.0 | Sign and Notarize Proposal Form | Acknowledge all Addendums | No Qualification. Clarifications or Exclusion sho contract and give bond for the faithful performance the same to the principal, then this obligation shall t execute such contract and give performance bond shall, upon demand., forthwith pay to the obligee th hereof. Provided further, that the bid may be withdr ☐ Affidavit A or B ☐ Minority, Women, and Small Business Enterprise (SEAL) Viewed Contract Documents Drawings, Project Specifications, CMR Bid Man Clarifications (SEAL) All subcontractors are required to drop off their bid packa 2:00 PM, OR mailed-in bids must be received by Novembe Office: 763 Comtech Drive, Pembroke, NC 28372. _(SEAL) (SEAL) PLEASE PROVIDE INFORMATION TO CONTACT AFTER CMR 00 43 3 **Bid Check List**

Bid Form

	metcon
CMR 00 41 00 - Bid Proposal Forms	
Robeson Career and Technical Education	on Center, Planetarium and Science Center
BID PACKAGE # AND TITLE:	
BID PROPOSAL OF:(Hereinafter call "B	IDDER") (Name of Firm)
A(N) organize	ed and existing under the laws of the State of
BIDDER'S North Carolina STATE LICENS	
The bidder, in compliance with the Instructi	on to Bidders for the above referenced project – Bid Package, Ilments including plans, specifications, and addenda issued by
metcon ist Doors and Hardware)	beon, Construction Manager, dated (Date) and being familiar requirements, and with all of the conditions surrounding the ding availability of materials and labor, hereby proposes to imits, fees, taxes, insurance, bonds if required, scaffolding, stransportation, supervision, clean-yan ad safety measures lecessary to provide the entire scope of work included in this rioss indicated on this Form of Proposal. Those priors are to e work required for this Bid Package Scope of Work including
.00	s read and familiarized him or herself with the Minority, Program, and further agrees to fully incorporate and r has also completed and attached to this bid proposal;
ould be written on Bid Form	fforts" or "Affidavit 2 – Intent to Self-Perform"
e Identification Form sual (Scope of Work), Addendums and age at the bid opening location before er 20, 2023, by 5:00 PM to PEMBROKE	acceptance of the bid is mailed or delivered to the undersigned due date , to enter into a Subcontract Agreement with the discated in the appropriate spaces on this form, which is based and specifications, addends, the Bid Manual, and the Scope (x, and including work that might be considered a part of this eofficially indicated herein. The bidder further agrees to, within instruction Manager a contract properly executed, insurance
l documents enclosed inside the envelope. SED ENVELOPE. BID	and Labor & Material Payment Bond. ed, and evaluated by the Construction Manager, and the sole determined, said Bidder agrees to meet immediately of determining that the Bidder has included a complete scope see meetings, the Bidder agrees to provide herein a complete, blootriactors, a list of all Suppliers, a schedule of anticipated their manufacturers proposed for use in the work as required
	CMR 00 41 00 Page 23

Addendums, Alternates, & Unit Prices

		_	,		
	metcon		Robeson Career and Technical Education Center.	Planetarium and Science Center	tcon
The Bidder acknowledges receipt of the following Addenda is Addendum NoDated:	sued by the Construction Manager:		acceptance of the alternate, the words "Zero" Please do not leave BLANK.	and a dollar figure. If the base bid is not chang , "No Change", "N/A" or Not Applicable is acce	ed by the ptable.
Addendum NoDated:				ates and cover page of drawings for details	
Addendum NoDated:			Alternate No. 1 - Planetarium:		
SASE BID The undersigned agrees to perform the entire Scope of Work for the contract Documents, Addenda, and Bid Manual. Pricing is to be p	nis Bid package, as described in the rovided as follows:		ALTERNATE NO. 1A Planetarium Provi a. Provide turn-key Planetarium system: C	der (Owner Preferred) osm, no substitutions.	Dollars,
tem 1 - Base Bid:), Circle one Add or Deduct	
	Dollars,		(9		
<u>,</u>			ALTERNATE NO. 1B Planetarium Provi a. Provide turn-key Planetarium system: R	der (Owner Preferred) SA, no substitutions.	
em 2 - Performance and Payment Bonds (if not required inse					Dollars,
	Dollars,		(S), Circle one Add or Deduct	
, .					
-			ALTERNATE NO. 1C – Planetarium Provid	er (Owner Preferred)	
tem 3 - (Total of Item 1 and 2):			a. Provide turn-key Planetarium system: S	SIA, no substitutions.	
	Dollars,				Dollars
s			(\$), Circle one Add or Deduct	
ihow amount in both words and figures, in case of discrepancy, th	e amount shown in words shall govern.				
Il North Carolina State Sales and Use Taxes or Local Sales an			ALTERNATE NO. 1D – Planetarium Provid a. Provide turn-key Planetarium system: Z	er (Owner Preferred) eiss, no substitutions.	
ase Bid and Alternates (including taxes on purchased or rental at this bid will remain good and may not be withdrawn for a peri	of tools and equipment). Bidder agrees			¬	Dollars
at this bid will remain good and may not be withdrawn for a peri Bid Proposal.	od of ninety (90) days after receipt date), Circle one Add or Deduct	
		etarium and Scien	ce Center metcon	a circle one Abb or Debbe	
		na I Init Brises he	ive been identified. Provide the unit cost		
		n this contract. P	rices are to include all direct cost of the stracts, materials, labor, etc. Prices shall		Dollars
		ect. Unit prices w	vill be used as a basis for adjustment of). Circle one Add or Deduct	
CMR 00 41 00		corresponding t	ce must be provided in the appropriate to your bid package.		
Page 24		pelow. Constructi ge.	on allowances, if required, are included	0 41 00 e 25	
				1125	
Bio	ider has reviewed the proposed Schedule	included in the bid ma	anual and agrees that it can achieve the		
CC	INTRACT TERMS AND CONDITIONS				
Bio do	ider has read and reviewed the terms and cuments enumerated in the Table of Conte enter into Subcontract with the Construction	ints of the Bid Manual	in the contract documents including all and takes no exception and is prepared		
Th	e undersigned represents that this propose any kind with any other bidder of the same	al is made in good faith	h, without fraud, collusion, or connection		
his	ther own behalf, without connection of ob interest in regard to all conditions pertain	digation to an undisci	losed person; that no other person has		
do	ne, has made his/her own examination dersigned understands that the Constructi	and estimates and	from them makes this proposal. The		
an	and all Bid Proposals and to waive any in	rregularities or inform	and Architect reserve the right to reject alities.		
	SNATURE:				
	wner, President, or Authorized Agent if Co MF & TITLE:	rporation)			
NA	me a mee:				
2**	SIGNATURE: (Print)	WITNESS:			
-	(If Partnership)				
BL	SINESS ADDRESS:				
(8)	reet Number & Street, PO Box)				
	ty, State, Zip, Phone)		·		
	ty, State, Zip, Phone) TEST (if Corporation)				
	(Name)	(Title)	_		
	,,				
Ch	eck One: Individual Partnership	CMR 00 41 00	Affix Corporate Seal Here		
		Page 26			

Project Prequalification Submittal





Bid Documents

BID COMPLIANCE Minority, Women, and Small Business Program

County of	
Affidavis o	(Name of Binder)
Bidder m	I have made a good faith effort to comply under the following areas checked: ast earn at least 50 points from the Good Faith Efforts list for their hid to be considered responsiv
that w	Peints) Contacted minority businesses that reasonably could have been expected to submit a quote and are known to the contractor or available on State or local government maintained lists, at least 10 days the hid date and notified them of the nature and scope of the work to be performed.
2 - (1) prospe	Points) Made the construction plans, specifications and requirements available for review by citive minority businesses, or providing these documents to them at least 10 days before the bids are due
3-(15	Points) Broken down or combined elements of work into communically feasible units to facilitate ty participation.
Histor of min	Points) Worked with minority trude, community, or contractor organizations identified by the Office of cally Underutifized Sestingues and included in the bid documents that provide assistance in recruitmentrify businesses.
	Points) Attended pre-bid meetings scheduled by the public owner.
☐ 6 - (2) or inse	Points) Provided autistance in getting required bunding or insurance or provided alternatives to bonds rance for subcontractors.
unque	Points) Negociated in good faith with interested minority businesses and did not reject them as find without sound reasons based on their capabilities. Any rejection of a minority business based on qualification should have the reasons documented in writing.
capital	Points) Provided assistance to an otherwise qualified minority business in need of equipment, loss lines of credit, or joint pay agreements to socure foams, supplies, or letters of credit, including waiving the ordinarity required. Assisted minority businesses in obtaining the same unit pricing with the expellers in ordinarity return to long minority businesses in establishing ordinarity.
9 - (20 increas possib	Points) Negotiated joint venture and parametrisp arrangements with minority businesses in order to copportunities for minority business perfectpation on a public construction or repair project when c.
10 - (2 tracet c	0 Points) Provided quick pay agreements and policies to enable minerity contractors and suppliers to asti-flow demands.
agreement schedule o provision t the terms	res with CSSA-128-144 and Done of Education Colley the underlying with other into a formal with the firms before in the described not of Huerry, Wenne and Small Business Participation with the firms before in the described not of Huerry, when and Small Business Participation Colleges and the Colleges of Huerry Participation of the Contract The Colleges of Huerry Participation of the Contract The One-of-traction Participation Participa
Date:	Name of Authorized Officer:
	Signature:
	Title:
(AL State of County
\ SE	Subscribed and sworn to before me this day of 26
\	
-	Notary Public My commission expires
MWSBE G	eldelines 3003-Rev 04,17.15

✓ MWSBE ID Form

✓ Affidavit A or Affidavit B

	Attach AFFIDAVIT A or AFFIDAVIT B to the Bid
	State of North CarolinaAFFIDAVIT B- Intent to Perform Contract with Own Workforce.
	Afficavil of
	(Manua of Cudder) Literately out if if that it is not inster to perform 100% of the work required for the
	(Name of Project)
	In custing the confidence, the blocker actors consists of blader does not removarily subscorrect electronic of bits types grapes, and meaning performs and not be compatible of confidence and will begin the distinguishment of the blocker of the blocker of the confidence and the grapes with higher count contrast such, success AND the biblior of I non-mortages that materials or supplies to the professionation of the country.
	The Hidder space to provide any additional information or enumerabilities requested by the eveter in support of the stone statement.
	The andmigned hotely could write by or she has read this confliction and it is authorized to black the Bidder or the storms to win contained.
	Onder Name of Authorized Officer
	Signature:
	SFAL.
	State-of
	Noary Prists My countries capites
ı	f you are ordering ANY material or
S	upply, using labor or transport, you
	CAN NOT submit Affidavit B
	WWSRS (Lottelines 2003-Zev 04.11: 15

Project MWSBE Compliance





Documents

Bid

BID COMPLIANCE Minority, Women, and Small Business Program

AFEIDAYTI D — Good Paith Efforts Canaly of Met Loburg If the aspirational goal of MRE 10%, Well Ois, and SBE 5% in Construction, and/or MBE 5%, and SBE 5% is Other toward reposition, responsible to the Construction and Constru

County of			renormed by	M/W/SBE Firms
	TO BE SUBMITTED ONLY BY THE	APPA	RENT LOWEST RESP	ONSIVE RIDDERS
f the portion of the work to be ex- Policy is agual to or greater than to MBE 5%, WBE 4%, and SBE 5% sidders total contract price, then of	couted by M/WBE firms as defined in G be M/WSBE aspirational goal of MBE in Other Services und/or MBE 3%, WE hin bidder must complete this affidavit. I hin 72 hours after notification of being	\$143-12 10%, W. 3E 3%, : hls aftir	18.2(g) and Board of Edu BE 6%, and SBE 5% in C and SBE 5% in Goods po tayit shall be provided by	eation M/W/SBE enstruction, and/or ricipation of the
Allidavit of	(Name of Bidder)		I do hereby cer	ify that on the
2.2.300	(Name of Bidder)			
	(Project Name)			
	Amount	enie e		
will expend a minimum of	% of the total dollar amount of the construction subcontractors, vendors, sup	ontract ·	with minority, women, or	small business enterprises
se subcontracted to the fallowing	Corner Noted Indiana		Assessed and distanced advances in	roquired
Name and Address	*M/9	//SBE	Week description	Dollar Value
	Care	gory		
		-		
		-		
	-	_		
		-		
		_		
	s: Black, African American (B), Hispani N), Femsle (B) Socially and Economical			e American Indian
formal agreement w contract with the O The undersigned be	GS143-128.2(d) and Board of Edu with the firms for work listed in this ware. Failure to fulfill this commi- creby certifies that be or she has re- erprise commitment and is authori	s sched tment i ad the	ule conditional upon on may constitute a bread terms of the Minority	execution of a ch of contract. Women, and
herein set forth.	Authorized (Mileer			
herein set forth.	Authorized ()fficer:			
herein set forth.				
herein set forth.				
herein set forth.	Signature:			
herein set forth.	Signature:			
herein set forth.	Signature: Title: State of Subscribed and swara to before me			
herein set forth.	Signature:	County		
herein set forth.	Signature:	County		

	۸ ۲	· .			,
✓	Af	tid	lav	Ίŧ	(

- ✓ Affidavit D
- ✓ Appendix V

	APPENDIX V WAIVER REQUEST FOR GOOD FAITH EFFORTS	
PROJECT:		
ADDRESS:	STATE: PHONE NO:	ŻIP:
	() or Portial () waiter for the MOW/SILL	aspirational goals for this particular
project for the fullowing reasons:		
Signature:	Date:	200 - 200 - 1
	,	
Good Paith Efforts Verificat:	CMS USE ONLY	
Request of Walver Granted: Community	YES ()NO ()	
	Da	













BUILDINGS INFRASTRUCTURE







Pamlico County School 6-12

Prebid Meeting

June 27, 2024

Tony 1:54 PM

Jim Brown

John Greig to Everyone 1:54 PM

John Greig johngreig@a1glassnc.com A1 Glass and Aluminum

4seasonsdemo to Everyone 1:54 PM (Edited)

4 Seasons Demolition. Valarie Fowler val@4seasonsdemo.com 910-793-3662

Connor Berryman to Everyone 1:54 PM

Connor Berryman

Tony to Everyone 1:54 PM

Solara of the Carolinas 910-723-1270

John Spruill to Everyone 1:54 PM

John Spruill B.E. Singleton & Sons, Inc. john@besingleton.com 252-508-6912

TONY BROWN to Everyone 1:54 PM

TONY BROWN

Connor Berryman to Everyone 1:54 PM

Connor Berryman; commonwealth blinds and shades; connorb@commonwealthblinds.com

cfischer to Everyone 1:54 PM

Colton Fischer Colton@brinnglass.com

TONY BROWN to Everyone 1:54 PM

SOLARA OF THE CAROLINAS

Darren.Warwick to Everyone 1:54 PM

Darren Warwick Acousti Engineering darrenwarwick@acousti.com

You to Everyone 1:55 PM

email Phone company and name

Triston to Everyone 1:55 PM

Triston Arwood - North State Steel - 252-830-8884 - triston@northstatesteel.com

Kendra Blackmon to Everyone 1:55 PM

Kendra Blackmon - Rush Masonry

kblackmon@rushconstruction.org

910-200-0362

Brian to Everyone 1:55 PM

Brian Sherwood - ECS brian.sherwood@ecscontrols.net

Connor Berryman to Everyone 1:56 PM

Connor Berryman; Commonwealth blinds and shades; 804-746-9112 x 818; connorb@commonwealthblinds.com

Fernando Nanita to Everyone 1:56 PM

Heartland Acoustics Fernando Nanita Fernando. Nanita@heartland-acoustics.com 919-636-7957

cfischer to Everyone 1:56 PM

Colton Fischer - (252) 515-6881 - Brinn Glass, Inc. - Colton@brinnglass.com

Lucas Probst to Everyone 1:56 PM

Lucas Probst - Stevens Industries, lucasp@stevensind.com (217) 240-5594

TONY BROWN to Everyone 1:57 PM

TONYBROWN@SOLOARANC.COM 910-584-6931 SOLARA OF THE CAROLINAS

Will Hollowell to Everyone 1:57 PM

Will Hollowell - GlassTech Commercial Glazing Services, Inc. - whollowell@glasstechonline.com - 252-355-9195

Craven Glass - Emma Hardy to Everyone 1:57 PM

Emma Hardy - Craven Glass Co emma@cravenglasscompanyinc.com (252)637-3761

Dave Savary to Everyone 1:57 PM

Dave Savary - Baker Mechanical Inc 252-236-8809 dsavary@bakermechanicalinc.com

Cindy Hodge to Everyone 1:57 PM

Cindy Hodge; Clayton Commercial Glazing, cindy@claytoncommercial.net 919-550-4024

Chris A. to Everyone 1:57 PM

Chris Anderson

Chris A. to Everyone 1:57 PM (Edited)

Allcon Roofing 828-405-2915 canderson@allconroofing.com

JJ Daugherty to Everyone 1:58 PM

j.daugherty@nationalcoatingsinc.com

Charles Ryan Buhl to Everyone 1:58 PM

Ryan Buhl - DH Griffin Wrecking - 732 320 8666 - crbuhl@dhgriffin.com

Learning Environments to Everyone 1:58 PM

Riley Mumford - Learning Environments, Inc. - rmumford@lecarolina.com

Kayla.Lewallen to Everyone 1:58 PM

Kayla Lewallen - Keller North America, Inc.

Edwin Smith III to Everyone 1:58 PM

Edwin Smith III - Retro Environmental

DB to Everyone 1:58 PM

David Brohl - Nycom

Kaputo to Everyone 1:58 PM

Melisssa Open Door

Donnie Dautry to Everyone 1:59 PM (Edited)

Donnie Autry - East Carolina Mechanical Phone # 910 - 333 - 8680 ext. 3007 email-dautry@ecmechanical.biz

Dave Porter to Everyone 1:59 PM (Edited)

Dave Porter - TA Woods (910) 367-6087 dporter@tawoods.com

Ben Price and Jason Boyle to Everyone 1:59 PM

Ben Price

Curt Ervin to Everyone 1:59 PM

LJ Electrical Company, Curt Ervin, Broc Gremminger, 252-526-7013, curt@ljelectricalcompany.com

Blake Einhellig to Everyone 1:59 PM

Blake Einhellig - Concordia Building company- (919) 762 7366,

elip to Everyone 2:00 PM

Eli - Chef's Depot

Ben Price and Jason Boyle to Everyone 2:00 PM

Southeastern Contracting, Inc.

540-808-5345

ben@southeasterncontractinginc.com

Ben Price

Superior Concrete - Mason Deal to Everyone 1:55 PM

Superior Concrete of NC Inc. 252-215-1060

Superior Concrete - Mason Deal 1:55 PM

brandon@sciofnc.com

mason@sciofnc.com

Triangle Roofing Services, Inc Brad Shaltz to Everyone 2:00 PM

Triangle Roofing Services, Inc. Brad Shaltz Brad@Triangleroof.com 919-609-8246

Colin Regan to Everyone 2:01 PM

Colin Regan - CM Red - cregan@cm-red.com

Sarah Ide to Everyone 2:01 PM

Sarah Ide

Raleigh East Concrete

Sarah@raleigheastconcrete.com

Joshua Hey to Everyone 2:01 PM

Yes Solar Solutions - Joshua Hey - jhey@yessolarsolutions.com 603-321-4932

Eddie Lester to Everyone 2:03 PM

Eddie Lester BM Roofing

Phillip Henry - TSI-Global to Everyone 2:04 PM (Edited)

Phillip Henry - phenry@tsi-global.com (919)-413-1390 ... TSI-Global - NC Certified MBE.

AV Integration, Security, Access Control, Data Cabling, Low voltage, Voice

Elijah Ammons to Everyone 2:04 PM

Elijah Ammons Barbour Brothers Construction

RMiller to Everyone 2:04 PM

Ron Miller, Steel Fab, York, SC

Irene Leonard to Everyone 2:05 PM

Janhery Acosta- Concordia Building Company LLC

ScottGordon to Everyone 2:05 PM

Scott Gordon - Enpuricon Inc. sgordon@enpuricon.com 919-524-4153, Abatement/Demo

Tamara (EMR) to Everyone 2:05 PM

Tamara Frank | EMR Services Inc | 336-807-6569 | tamara@emrservicesinc.com | Demolition & Abatement

mjones to Everyone 2:06 PM

Mike Jones, Steel Technology, mjones@steeltechnc.com

fvanosten to Everyone 2:06 PM

Fredrick Van Osten - Coreslab Structure

Eastern Corporation to Everyone 2:06 PM

Eastern Corporation

Ernie Song

estimating@usaeastern.com

919-562-8123

JJ Daugherty to Everyone 1:57 PM

JJ Daugherty - National Coatings

JJ Daugherty 2:06 PM

919.710.5682

Kayla G to Everyone 2:00 PM

Kayla Gore NJR Construction, LLC. kgore@NJR-construction.com

Kayla G 2:06 PM

980-237-0002 ext 102

Colin Regan to Everyone 2:06 PM

Colin Regan - CM Red - dreaugh@cm-red.com - 919-606-3638

Irene Leonard to Everyone 2:06 PM

Concordia Building Company LLC-Office@concordiabuilding.com- Janhery Acosta

Robert Coats - Grieme Roofing to Everyone 2:06 PM

Robert L. Coats Jr.

Lead Estimator

Grieme Roofing Company., Inc.

rcoats@griemeroofing.com

910-639-3263 mobile

910-944-9630 office

Isaac Martin to Everyone 2:06 PM

Isaac Martin - Berlin's Restaurant Supply - Isaac@berlins.com - 919.338.6586

Ashley Peace to Everyone 2:06 PM

Precision Walls - Ashley Peace apeace@precisionwalls.com

Kayla.Lewallen to Everyone 2:06 PM

Kayla Lewallen - Keller North America, Inc. kayla.lewallen@keller-na.com Contact Person: Joel Velez (Project Manager) joel.velez@keller-na.com

Carolina Classic Window & Glass to Everyone 2:06 PM

Carolina Classic Window & Glass

Nathaniel@ccwginc.com

Nathaniel H

336-553-2852

Todd Fromm -TSI to Everyone 2:07 PM (Edited)

Todd Fromm, TSI Global Companies LLC, MBE. tfromm@tsi-global.com, 636-425-1354, Audio-Video systems, security systems, low-voltage

Steele.Lloyd to Everyone 2:07 PM

Steele Lloyd, Keller North America.

fvanosten to Everyone 2:07 PM

Fredrick Van Osten - Coreslab Structure - fvanosten@coreslab.com 770-471-1150

Will S phone to Everyone 2:07 PM

Will Stewart

Green State Power

will@greenstatepower.com

336-430-5420

Steele.Lloyd to Everyone 2:07 PM

Steele.Lloyd@keller-na.com

Scott Hardeman to Everyone 2:07 PM

Scott Hardeman

K&R Building Solution to Everyone 2:07 PM

Trinity White

K&R Building Solution

twhite@krbldgsolution.org

(704)606-7914

Charles Davis to Everyone 2:08 PM

Earth Comfort LLC Charles Davis 912.695.7350

Edwin Smith III to Everyone 2:08 PM

Edwin "Tripp" Smith III | Retro Environmental - Abatement & Demolition | (910) 880-1027 | esmith@retroenvironmental.com

Mr George to Everyone 2:08 PM

George Hodges

3 Sons Steel Inc

George@3sons-steel.com

252.813.5389

Derek's iPhone (2) to Everyone 2:09 PM

Derek johnson

Foss demolition

Djohnson@fossdemolition.com

Ross Ritenour to Everyone 2:09 PM

Express Technologies Inc.

Scott Hardeman to Everyone 2:09 PM

Scott Hardeman/Southeast Geo Solutions/AIA Consultant Geothermal System 803-718-2135 scotth@southeastgeosolutions.com

Armghan Aslam to Everyone 2:10 PM

Armghan Aslam - 8MSolar - a.aslam@8msolar.com

Hine Sitework - Elayne Kincaid to Everyone 2:10 PM

Elayne Kincaid elayne@hinesitework.com 919-736-8990

wfraley to Everyone 2:11 PM

William Fraley CBD Casework Millwork

Ross Ritenour to Everyone 2:11 PM

Express Technologies inc, Ross Ritenour 540-419-4975 rritenour@express-tek.com

elip to Everyone 2:24 PM

Eli Potash

Clint Rouse to Everyone 2:24 PM

clintrouse@seegarsfence.com

Tom to Everyone 2:25 PM

Tom Keller, Yes Solar, tkeller@yessolarsolutions.com

Brad Reece to Everyone 2:25 PM

Brad Reece (252)917-3351 breece@h2igroup.com

wfraley to Everyone 2:25 PM

William Fraley - CBD Casework Millwork 239-821-3099 wfraley@cbdga.com

Brian Fariss to Everyone 2:26 PM

Brian Fariss- Eskola Roofing 704-519-7858 Bfariss@eskolaroofing.com

Jim Brown to Everyone 2:26 PM

Jim Brown - Solara of the Carolinas - jimbrown@solaranc.com 910-723-1270

elip to Everyone 2:26 PM

Chef's Depot ,Eli Potash , Elip@culinarydepot.com , 845-414-2230- Food Service Equipment

Elijah Ammons to Everyone 2:27 PM

Elijah Ammons, justin@barbourbrothers.com, Barbour Brothers Construction, (919)242-1266

Blake Einhellig to Everyone 2:28 PM

Blake Einhellig - Concordia Building company- (919) 762 7366, estimating@concordiabuilding.com

Jeff Smith to Everyone 2:32 PM

Jeff Smith

Graybar

919-525-5992

stevenjeffrey.smith@graybar.com

Joshua Hey to Everyone 3:16 PM

Note to all electrical subcontractors: please contact us if you need help with the Photovoltaic and/or the EV Charger Alternate Scope of Work. Joshua Hey, Yes Solar Solutions, jhey@yessolarsolutions.com 603-321-4932

K&R Building Solution to Everyone 3:25 PM

Rebecca Desmore

K&R Building Solution

rdesmore@krbldgsolution.org

(704)606-7914

Pamlico County School 6-12 Prebid 06.27.24

BUILDINGS INFRASTRUCTURE Company Name Fi	IR: First and Last Name	FIEDIU 00.27.24	Dhous Misselve
Barnhill Intracting	10008	Thorse of the state of the stat	
EMR Sources in	1/2	Lynes & Bornailleontracting Com	919 507 6061
NC Sound	11 -	Word & Crasco Classical Miles	253. 201.00 F.0
58 + 7	Brith And ERSon	34~0EBSON & 55.00.	0h28-952-252
			•
